

## Monthly Project Assessment Report – November 2021

### Independent Verification and Validation (IV&V) for the Implementation of the Highways Financial Management System Project

Author: Ohanasoft/IV&V Project Team  
Creation Date: December 02, 2021  
Last Updated: December 17, 2021  
Version: Final v1

**Version History**

Version Number	Updated By	Revision Date	Description of Change
Final v1	IV&V Project Team	12/17/2021	N/A

## Table of Contents

I.	Introduction and Summary .....	5
A.	Introduction.....	5
B.	Summary.....	6
II.	IV&V Dashboard.....	7
A.	Subject Category.....	7
B.	Observation, Risk, Issues, Subject Category .....	8
C.	Total Budget vs. Inception to Date Expenditure, Project Timeline .....	9
III.	IV&V Findings – Observations, Risk, Issue and Feedback/Mitigation.....	10
A.	Subject Category: Schedule Management .....	10
B.	Subject Category: Resource Management .....	12
C.	Subject Category: Quality Management .....	13
D.	Subject Category: Risk/Issue Management.....	14
E.	Subject Category: External Impact Management .....	14
F.	Subject Category: Requirement Management (Processes, Requirements and Fit/Gap) .....	15
G.	Subject Category: Solution Design and Configuration .....	19
H.	Subject Category: Interface and Integration .....	20
I.	Subject Category: Reports and Analytics .....	21
J.	Subject Category: Data Conversion .....	21
K.	Subject Category: Documentation .....	21
L.	Subject Category: Training and Knowledge Transfer .....	22
M.	Subject Category: Production Migration .....	23

IV. Meetings and Discussions Participated for the Month of November 2021 .....	24
V. IV&V Deliverables, Reports and Meetings Completed .....	27
VI. IV&V Deliverables, Reports and Meetings Planned To be Completed in Explore Phase.....	28
VII. Appendix .....	29
A. Impact Definition.....	29
B. Status Definition.....	29
C. Subject Category Definition.....	30
D. Observation, Risk, and Issues List.....	32

## I. Introduction and Summary

### A. Introduction

Department of Transportation Highways (DOTH) manages the planning, construction, and maintenance of the State of Hawaii's approximate 2,675 lane miles of highway on Oahu, Kauai, Maui, Lanai, Molokai, and Hawaii. DOTH's mission is to provide a safe, efficient, and accessible highway system through the utilization of available resources in the maintenance, enhancement, and support of land transportation facilities. DOTH's primary function is to plan, design, and supervise the construction and maintenance of the State's highway system.

DOTH commissioned an Enterprise Resource Planning (ERP) Contractor, LSI in March 2021 to provide an accounting system solution that would modernize certain State of Hawaii, Department of Transportation, Highways Division (DOTH) IT systems, associated systems, and business processes, including fully replacing DOTH's legacy Highways Financial Accounting System (HWYAC) and certain software components of DOTH Districts' AS400 systems.

The new DOTH Financial Management System (H4) will utilize SAP S/4HANA Cloud ERP and will cover DOTH Business Processes of Budget, General Ledger, Accounts Payable, Accounts Receivable, Lease Management, Fixed Assets, Procurement, Project & Grant, Federal Billing, Human Resources, Time and Labor, Payroll, Inventory Management, Plant Maintenance, Reporting, and Analytics.

DOTH also acquired a contract with IT Management Consulting Firm, Ohanasoft, to provide information technology independent verification and validation consulting services for the implementation of the DOTH Highways Financial Management System. The IV&V contractor's role is to provide an objective, neutral, third-party view of the implementation of the Highways Financial Management System with the intent of protecting the State's interests for success of the project. Throughout the system implementation, the IV&V team will perform ongoing project IV&V activities and will identify issues/deficiencies/risks with the System implementation project, provide feedback and recommendations for mitigation and improvement, and provide on-going reporting on project activities.



## B. Summary

The Explore Phase started on June 1, 2021 and initially was planned to be completed on September 30, 2021. However, explore phase has been extended a few times as more workshops were needed to discuss workflow and requirements, and deliverables need to be completed. In total, more than 40 workshops were held to discuss and review As-Is, To-Be, SAP functions, solutions, and DOTH requirements in November 2021. Currently there is no specific planned date set for the completion of the Explore phase. IV&V team is not confident that Go-Live date of July 1st, 2022 will be met.

Multiple turnovers of the project team members (Project Manager, Fund Management Consultant, Two Assistant Project Managers, FHWA Billing Consultant, Financial/Integration Lead) has been a factor for the slower than projected progress.

Waterfall funding has been a challenge for the consulting team to fully understand and to come up with an integrated solution involving all the corresponding modules.





































Project Design Documents (PDD), which documents DOTH functional areas along with business processes, to-be processes and their descriptions, configuration, relevant data, cross-functional impacts, and organizational change considerations, are one of the main deliverables for the Explore phase. PDD review process is challenging due to lack of SAP understanding and inefficiency in cross-referencing with the requirements. The preferred method would be to examine the RTM first and cross-reference the requirements with PDD.

DOTH team should request additional SAP training as needed, because we continue to observe team's struggle in following the sections of meetings. Some of the difficulty during the meeting sessions and understanding the deliverable documents stems from a lack of understanding of SAP functionalities, its solutions, and processes.

There was an effort initiating lists for action items in the Open Items Tracker and issue tracking in the Project Issue Log, however the effort became stagnant. For example, Open Items Tracker was last updated in August and Project Issue log often do not have specific detail resolution for the issues. There should be continued effort to update and monitor action items and issue tracking as part of the ongoing project management.

## II. IV&V Dashboard

### A. Subject Category



IV&V Dashboard – Subject Category			
Subject Area	Subject Category	Impact	
		Previous Month	Current Month
Project Management	Schedule Management		
	Resource Management		
	Quality Management		
	Risk/Issue Management		
	Organization Change Management		
	Communication Management		
	Contract Management		
	External Impact Management		
System Implementation	Requirement Management (Processes, Requirements and Fit/Gap)		
	Solution Design and Configuration		
	Interface and Integration		
	Reports and Analytics		
	Security		
	Data Conversion		
	Documentation		
	System Testing		
	Training and Knowledge Transfer		
	Production Migration		

## B. Observation, Risk, Issues, Subject Category


## IV&amp;V Dashboard – Observation, Risk, Issues, Subject Category

## Number of Total Observation, Risk, and Issues

## Number of Observation, Risk, and Issues by Status

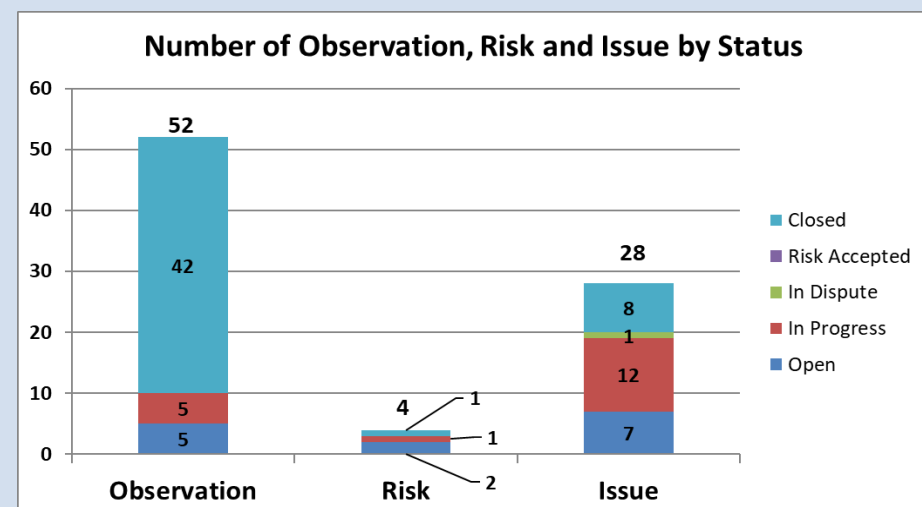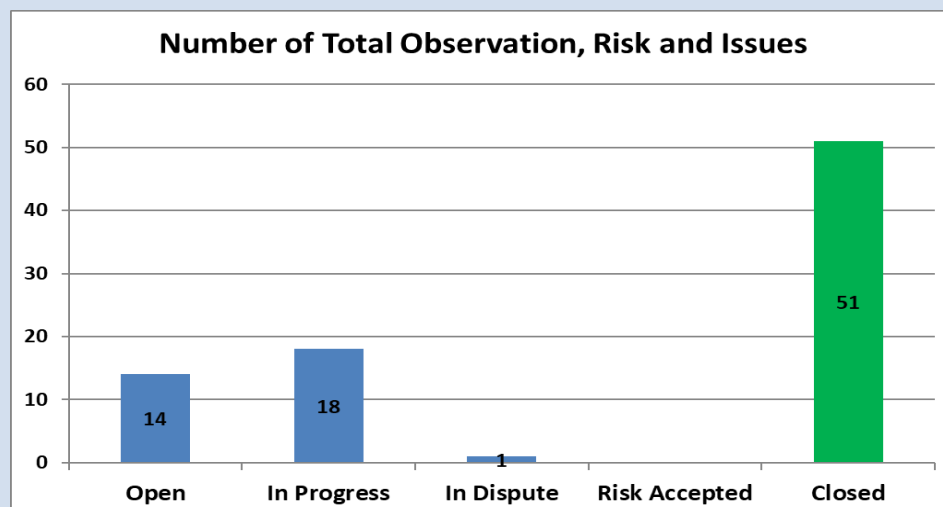

## Number of Observation, Risk, and Issues by Subject Category

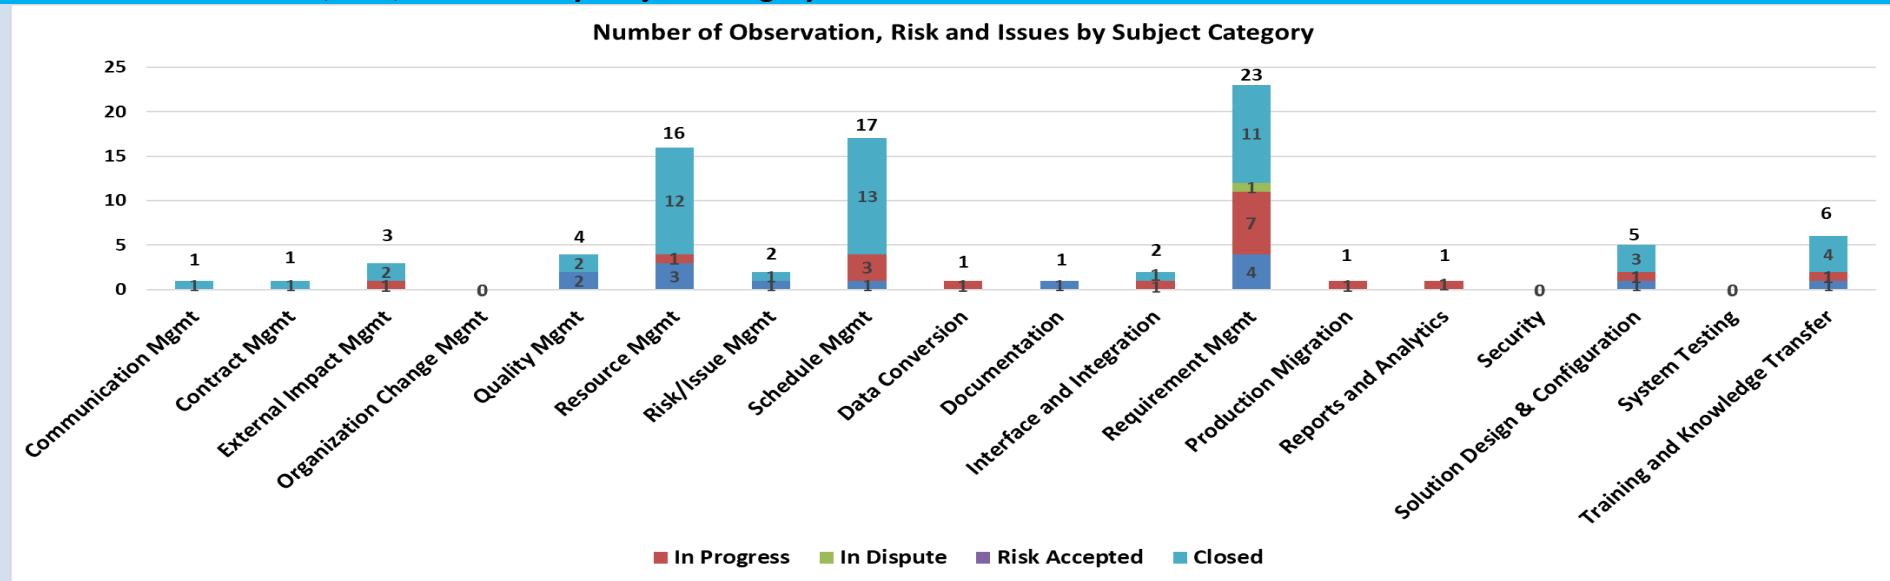




## C. Total Budget vs. Inception to Date Expenditure, Project Timeline

## IV&amp;V Dashboard – Total Budget vs. Inception to Date Expenditure and Project Timeline

## Total Budget Vs. Inception to Date (ITD) Expenditure

## Number of Observation, Risk, and Issues by Status

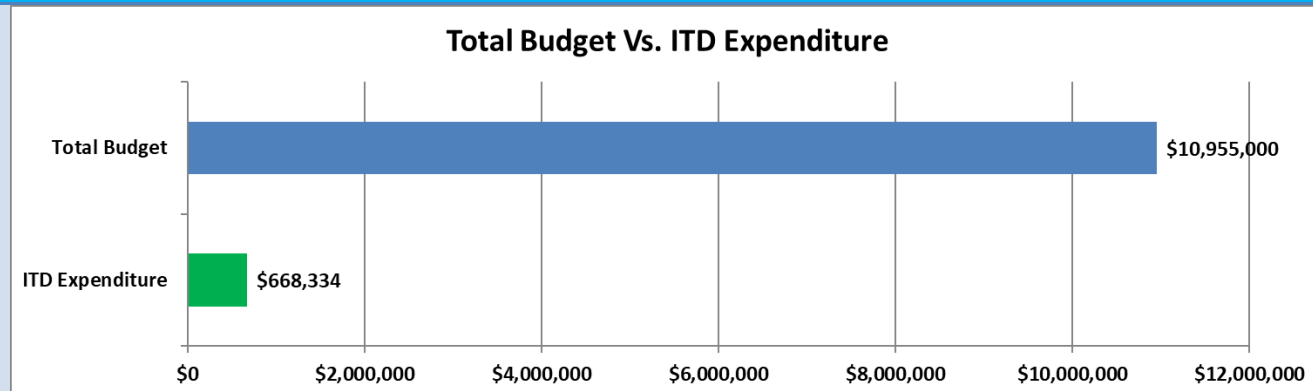

- Remaining Months: 10
- Completed Months: 9
- Percentage of Completed Months vs. Total Months: 47.37%
- Percentage of ITD Expenditure vs. Total Budget: 6.10%
- Remaining Budget Balance: \$10,286,666

## Project Timeline


DOTH Financial Management System (Wave I)	Mar-21	Apr-21	May-21	Jun-21	Jul-21	Aug-21	Sep-21	Oct-21	Nov-21	Dec-21	Jan-22	Feb-22	Mar-22	Apr-22	May-22	Jun-22	Jul-22	Aug-22	Sep-22
<b>Phase</b>																			
Prepare																			
Explore																			
Realize																			
Deploy																			
Production																			


**H4 is in the Explore Phase. The Explore Phase has been extended and there is no specific planned date set for its completion.**


- Prepare Phase: Define Strategy, Project Initiation, Project Standards, Technical Requirements.
- Explore Phase: Business Workshops and Requirements, Fit-Gap Analysis, Technical Solution Design, Testing Strategy, Training Strategy
- Realize Phase: Organization Alignment, Knowledge Transfer, Build, Development, Unit Test, Integration Test
- Deploy Phase: Support Plan, Training Delivery, Cutover Plan, User Acceptance, Simulations, Go/No-Go Decision
- Production: Cutover, Go-Live, Hypercare Support, Transition to Operations, Project Closeout

### III. IV&V Findings – Observations, Risk, Issue and Feedback/Mitigation

#### A. Subject Category: Schedule Management

Schedule Management: Observation, Risk, Issue and Feedback/Mitigation	
Issue	Impact
<p><b>ORI ID: I-210531-02</b></p> <p>The final Project Plan/Implementation Schedule has not been approved by DOTH and the deliverable is not completed. This is a foundational document for a project management and scheduling, and it is one of the most critical deliverables. Delay in the Project Plan and Implementation Schedule pose decreased confidence in being able to manage project resources efficiently and meet the final Go-Live date. Also, without the Project Plan and the Implementation Schedule DOTH has limited project visibility and it will impact schedule and resource management. It is currently unknown, at a detail level, if the number of resources are adequate to complete the project on schedule. Earlier versions of the Project Plan were not accepted partly because of oversubscribed resources and incorrect dates (i.e., one consultant or DOTH team member working more than 40 hours in a week, etc.)</p>	
Feedback/Mitigation/ Updates	
<p>It is recommended that LSI complete Project Plan/Implementation Schedule as soon as possible.</p> <p>Project Plan/Implementation Schedule Submission History:</p> <p>11/16/2020: The initial project plan was submitted and returned back to LSI after DOTH review due to incompleteness.</p> <p>12/21/2020: Updated project plan was submitted by LSI but returned back to LSI after DOTH review due to incompleteness.</p> <p>04/26/2021: Updated project plan was submitted by LSI but returned back to LSI after DOTH review due to incompleteness.</p> <p>06/14/2021: Updated project plan was submitted by LSI but returned back to LSI after DOTH review due to incompleteness.</p> <p>7/1/2021: Updated project plan was submitted by LSI but returned back to LSI after DOTH review due to incompleteness.</p> <p>8/4/2021: Updated project plan was submitted by LSI but DOTH requested a revision.</p> <p>9/02/2021: No updates have been submitted to DOTH. Revised Acceptance Date: 9/30/2021.</p> <p>9/16/2021: DOTH interviewed an assistant project manager candidate on 9/7/2021.</p> <p>9/30/2021: No updates have been submitted to DOTH.</p> <p>10/5/2021: LSI Assistant Project Manager submitted the revised project plan. DOTH has a meeting with the LSI Assistant Project Manager and requested a revision due to the project plan being incomplete.</p> <p>10/13/2021: LSI Assistant Project Manager submitted the revised project plan and DOTH will hold a review meeting on 10/22/2021.</p> <p>10/25/2021: DOTH had a meeting with the LSI Assistant Project Manager to review Project Plan/Implementation Schedule. Progress has been made, however some data such as the dates and % completion need to be corrected.</p> <p>11/10/2021: LSI Assistant Project Manager submitted the revised project plan and DOTH will hold a review meeting on 11/24/2021.</p> <p>11/24/2021: LSI Assistant Project Manager and DOTH Project Manager worked together via Teams and updated and fixed the Project Plan. There will be a follow up meeting.</p>	

Schedule Management: Observation, Risk, Issue and Feedback/Mitigation	
Issue	Impact
<b>ORI ID: I-210930-01</b> LSI extended the Explore Phase one month to complete the explore workshops and deliverables including Document Fit/Gap Analysis, Process Design Documents (PDD) (Documented Business Process Model), and Requirements Traceability Matrix.	
Feedback/Mitigation/ Updates	
Schedule should be reviewed and adjusted as needed. 10/15/2021: No major updates. 10/31/2021: It is extended again to the middle of November 2021. 11/18/2021: The Explore Phase has not been completed yet. 12/2/2021: The Explore Phase has not been completed yet. There is no specific target date forecasted by LSI.	

Schedule Management: Observation, Risk, Issue and Feedback/Mitigation	
Risk	Impact
<b>ORI ID: R-211028-01</b> The Go-Live date of 7/01/2022 may not be feasible due to: <ul style="list-style-type: none"> <li>- Delays in deliverables.</li> <li>- Lack of solution design for DOTH critical core requirements</li> <li>- Lack of focus on DOTH critical core requirements.</li> <li>- Multiple core staff turnover (Project Manager, Fund Management Consultant, Two Assistant Project Managers, FHWA Billing Consultant, Financial/Integration Lead)</li> </ul>	
Feedback/Mitigation/Updates	
It is recommended that: <ul style="list-style-type: none"> <li>- Outstanding deliverables should be completed as soon as possible.</li> <li>- DOTH critical core requirements solution design needs to make progress.</li> <li>- DOTH critical core requirements should be higher priority.</li> <li>- Reasons for high turnover should be evaluated and the H4 Project Team should take proper action.</li> </ul> 11/18/2021: No major updates. 12/2/2021: No major updates.	

**Schedule Management: Observation, Risk, Issue and Feedback/Mitigation****Issue****Impact****ORI ID: I-211028-10**

The Project Management Plan was delayed and has not been completed.

**Feedback/Mitigation/ Updates**

It is recommended that LSI complete the deliverable as soon as possible.

11/18/2021: No major updates.

12/2/2021: No major updates.

**B. Subject Category: Resource Management****Resource Management: Observation, Risk, Issue and Feedback/Mitigation****Observation****ORI ID: O-210826-01**

According to LSI responses to the requirements of Budget Preparation and Budget execution, Budget and Planning (SBP) module was proposed. However, solution design is developed in Fund Management module because SBP will not be available when Wave I goes live on 7/1/2022. The SBP is scheduled to go live on 8/1/2022, one month after the Wave I Go-Live date.

**Feedback/Mitigation/Updates**

It's recommended that LSI provide clear direction and roadmap for how FM will be used instead of SBP during the transition period between Wave I Go-Live and Wave II Go-Live.

10/15/2021: No major updates.

10/31/2021: No major updates.

11/18/2021: No major updates.

12/2/2021: No major updates.

**Resource Management: Observation, Risk, Issue and Feedback/Mitigation****Observation****ORI ID: O-211031-01**


There are turnovers in LSI project team members. Some team members need more time to understand information related to FHWA and DOT processes.


**Feedback/Mitigation/Updates**

LSI and DOTH should confirm that the consultants meet the qualifications as stated in the RFP, which includes FHWA experience and DOTH equivalent work experience.


11/18/2021: No major updates.


12/2/2021: No major updates.

Resource Management: Observation, Risk, Issue and Feedback/Mitigation	
Issue	Impact
<b>ORI ID: I-211115-01</b> Waterfall funding/Split is a core critical requirement for H4, however Waterfall funding/Split was not discussed as much as it should be throughout the Explore Phase. It only started to be discussed recently as an integrated solution during FHWA Billing session.	
Feedback/Mitigation/Updates	
It is recommended that waterfall funding/Split solution be designed by LSI as soon as possible. 12/2/2021: A whiteboard session is scheduled on 12/8/2021. DOTH is doing another presentation on how DOTH processes Waterfall funding/Split.	

Resource Management: Observation, Risk, Issue and Feedback/Mitigation	
Issue	Impact
<b>ORI ID: I-211115-02</b> Workshops related to Split/Waterfall funding require all consultants to participate because this requirement impacts the various DOTH requirements, including procurement, invoice, payroll, timesheet, project, etc. However, some consultants did not attend the Split/Waterfall-related workshops.	
Feedback/Mitigation/Updates	
FHWA Billing Process starts from cost collection where participation costs are incurred. It involves Fund Management, Requisitions, Purchase Orders, Accounts Payables, and General Ledger. Therefore, respective consultants should attend FHWA related meetings to collaborate and to develop an integrated solution for waterfall funding and FHWA billing. 12/2/2021: No major updates.	

## C. Subject Category: Quality Management


Quality Management: Observation, Risk, Issue and Feedback/Mitigation	
Issue	Impact
<b>ORI ID: I-211202-01</b> Some LSI Deliverables contained errors and misinformation such as incorrect project name, other client's system architecture, missing/incomplete contents, etc. E.g., Technical Infrastructure Plan/Design, Project Standard Strategy, Scope Management Strategy, etc.	
Feedback/Mitigation/Updates	
It is recommended that deliverables are more carefully prepared, reviewed and proofread by LSI document quality team before submitting to DOTH for review.	

Quality Management: Observation, Risk, Issue and Feedback/Mitigation	
Issue	Impact
<b>ORI ID: I-211202-02</b> Consultants worked on PDDs based on their responsible business areas. However, Process Flows Diagrams are not standardized in PDDs	
Feedback/Mitigation/Updates	
N/A	

## D. Subject Category: Risk/Issue Management

Risk/Issue Management: Observation, Risk, Issue and Feedback/Mitigation	
Observation	
<b>ORI ID: O-211028-02</b> Some items from issue log are being discussed without detailed resolution or follow-up.	
Feedback/Mitigation/Updates	
It is recommended that the issue log be reviewed and discussed in more detail with proper LSI resources and resolution should be discussed the PMO meeting. A separate meeting or inviting the proper LSI resource during the PMO meeting may be required. 11/18/2021: No major updates. 12/2/2021: No major updates.	

## E. Subject Category: External Impact Management

External Impact Management: Observation, Risk, Issue and Feedback/Mitigation	
Risk	Impact
<b>ORI ID: R-210812-01</b> DOTH FMS is required to be compatible with DAGS's future statewide financial system. A meeting with DAGS was held on 8/12/2021 and DOTH and DAGS discussed the new UCOA. However, the new UCOA is still under development at DAGS and the incomplete UCOA at DAGS could cause DOTH some rework after the new statewide financial system goes live. The implementation project for the statewide financial management system has not started yet and Go-Live date has not been determined either.	

**External Impact Management: Observation, Risk, Issue and Feedback/Mitigation****Feedback/Mitigation/Updates**

It is recommended that additional meetings are scheduled for further discussion and clarification of the new UCOA including the latest UCOA contents, changes, updates, and confirm a crosswalk between the FAMIS account codes and the new UCOA.

9/16/2021: No additional meetings with DAGS were scheduled.

9/30/2021: No updates.

10/15/2021: No updates.

10/31/2021: No updates.

11/18/2021: LSI and DOTH discussed if UCOA is the best fit for DOTH. Another meeting is scheduled on 11/29/2021.

11/30/2021: LSI and DOTH discussed H4 COA and agreed that LSI will perform more analyses and update/fix H4 COA.

**F. Subject Category: Requirement Management (Processes, Requirements and Fit/Gap)****Requirement Management: Observation, Risk, Issue and Feedback/Mitigation****Observation****ORI ID: O-210729-04**

DOTH critical core requirement, "Link Project Cost to Specific State Appropriation" started being discussed in Explore Workshops, however there are more details to be covered. Explore is in progress. A high-level solution design is scheduled to be developed and confirmed by DOTH in the Explore Phase.

**Feedback/Mitigation/Updates**

9/2/2021: No major updates.

9/30/2021: There were discussions in Explore Workshops and preliminary design is being developed.

10/15/2021: No major updates.

10/31/2021: No major updates.

11/18/2021: Discussions are in progress. No major updates.

12/2/2021: Discussions are in progress. No major updates.

**Requirement Management: Observation, Risk, Issue and Feedback/Mitigation****Observation****ORI ID: O-210729-05**

DOTH critical core requirement, "Accounting for Appropriated, Allotted, and Cash Authority" started being discussed in Explore Workshops, however there are more details to be covered. Explore is in progress. A high-level solution design is scheduled to be developed and confirmed by DOTH in the Explore Phase.

**Requirement Management: Observation, Risk, Issue and Feedback/Mitigation****Feedback/Mitigation/Updates**

9/2/2021: No major updates.

9/30/2021: There were discussions in Explore Workshops and preliminary design is being developed.

10/15/2021: Discussions are in progress. No major updates.

10/31/2021: Discussions are in progress. No major updates.

11/18/2021: Discussions are in progress. No major updates.

12/2/2021: Discussions are in progress. No major updates.

**Requirement Management: Observation, Risk, Issue and Feedback/Mitigation****Observation****ORI ID: O-210729-06**

DOTH critical core requirement, "Labor Compression" started being discussed in Explore Workshops, however there are more details to be covered. Explore is in progress. A high-level solution design is scheduled to be developed and confirmed by DOTH in the Explore Phase.

**Feedback/Mitigation/Updates**

9/2/2021: No major updates.

9/30/2021: There were discussions in Explore Workshops and preliminary design is being developed. Payroll interface was discussed in the meeting with ETS on 9/28/2021.

10/15/2021: Discussions are in progress. No major updates.

10/31/2021: Discussions are in progress. No major updates.

11/18/2021: HIP Interface discussions with ETS are in progress.

12/2/2021: Discussions are in progress. No major updates.

**Requirement Management: Observation, Risk, Issue and Feedback/Mitigation****Observation****ORI ID: O-210729-07**

DOTH critical core requirement, "The State Financial Accounting System" started being discussed in Explore Workshops, however there are more details to be covered. Explore is in progress. A high-level solution design is scheduled to be developed and confirmed by DOTH in the Explore Phase.



**Requirement Management: Observation, Risk, Issue and Feedback/Mitigation****Feedback/Mitigation/Updates**

9/2/2021: No major updates.

9/20/2021: There was a FAMIS Interface discussion with ETS.

10/15/2021: Discussions are in progress. No major updates.

10/22/2021: LSI and DOTH had a meeting with DAGS to discuss FAMIS interface. Email correspondents were exchanged as follow-up.

11/4/2021: LSI and DOTH had a meeting with DAGS and ETS to discuss interface between FAMIS and H4.

11/10/2021: DOTH had a meeting with eWorld to discuss possibility of downloading FAMIS data from DataMart.

12/2/2021: No major updates.

**Requirement Management: Observation, Risk, Issue and Feedback/Mitigation****Issue****Impact****ORI ID: I-211021-03**

It is difficult for DOTH to determine if all of DOTH requirements are properly addressed and included in the correct sections in PDD since they are not cross-referenced in RTM and the requirements are not listed/referenced sequentially in PDD.

**Feedback/Mitigation/Updates**

It is recommended that when PDD is submitted the corresponding section/module of RTM needs to be completed for DOTH to track requirements coverage, since RTM is referencing PDD.

10/28/2021: LSI project manager stated PDD is to be completed first and RTM is a result of PDD, also PDD is a living document and if there are requirements from RTM that were missed then they will be updated in PDD.

11/18/2021: No major updates.

12/2/2021: No major updates.

**Requirement Management: Observation, Risk, Issue and Feedback/Mitigation****Issue****Impact****ORI ID: I-211028-02**


The Requirements Traceability Matrix was delayed and has not been completed.


**Feedback/Mitigation/Updates**

It is recommended that LSI complete the deliverable as soon as possible.

11/18/2021: No major updates.


12/2/2021: No major updates.

Requirement Management: Observation, Risk, Issue and Feedback/Mitigation	
Issue	Impact
<b>ORI ID: I-211028-04</b> The Process Design Documents (PDD) (Documented Business Process Model) was delayed and has not been completed.	
Feedback/Mitigation/Updates	
It is recommended that LSI complete the deliverable as soon as possible. 11/18/2021: No major updates. 12/2/2021: No major updates.	

Requirement Management: Observation, Risk, Issue and Feedback/Mitigation	
Issue	Impact
<b>ORI ID: I-211028-09</b> The Document Fit/Gap Analysis was delayed and has not been completed.	
Feedback/Mitigation/Updates	
It is recommended that LSI complete the deliverable as soon as possible. 11/18/2021: No major updates. 12/2/2021: No major updates.	

Requirement Management: Observation, Risk, Issue and Feedback/Mitigation	
Observation	
<b>ORI ID: O-211103-01</b> Plant Maintenance implementation should not affect Go-Live on 7/1/2021.	
Feedback/Mitigation/Updates	
It is recommended that Plant Maintenance development is scheduled in order to not negatively impact Go-Live date for Wave I. It can go live with Wave II (or it can have its own schedule/Wave). Meanwhile, a manual upload of plant maintenance financial data to GL may need to be considered. 12/2/2021: LSI is reviewing a solution for Plant Maintenance Go-Live date.	

**Requirement Management: Observation, Risk, Issue and Feedback/Mitigation**


Issue	Impact
<p><b>ORI ID: I-211108-01</b></p> <p>Budget and Planning (SBP) is a part of the H4 solution and it is supposed to encompass budget transactions, including DOTH's budget prep, execution, A-15, A-19, and A-21. However, LSI proposed that solution design for A-15, A-19, and A-21 will remain in Funds Management until Budget and Planning consultant is available in the future. The H4 Project Team with the SBP consultant will determine the best solution for processing budget maintenance requirements: A-15, A-19, and A-21.</p>	
<p><b>Feedback/Mitigation/Updates</b></p> <p>It is recommended that H4 Project Team design a permanent solution that will best fit DOTH budget requirements from its first design by engaging the SBP consultant, instead of postponing designing the solution.</p> <p>12/2/2021: No major updates.</p>	

**Requirement Management: Observation, Risk, Issue and Feedback/Mitigation**

Observation
<p><b>ORI ID: O-211115-01</b></p> <p>A back-end split waterfall funding solution for FHWA billing is generally more common in the Department of Transportation Highways. However, the Department of Transportation Highways in Hawaii runs on a front-end split waterfall funding with many funds/appropriations. During the procurement process of a new DOTH Financial Management System, LSI proposed and confirmed that a front-end split waterfall funding would fit DOTH's requirements the best. When H4 project started, the financial lead took leadership and discussed a broad overview of how the future front-end split waterfall funding could work in SAP. Soon after, the financial lead left H4 project and LSI confirmed again that a front-end split waterfall funding is still the best solution for DOTH.</p>
<p><b>Feedback/Mitigation/Updates</b></p> <p>12/2/2021: No major updates.</p>

## G. Subject Category: Solution Design and Configuration

**Solution Design and Configuration: Observation, Risk, Issue and Feedback/Mitigation**

Issue	Impact
<p><b>ORI ID: I-211028-08</b></p> <p>The Technical Infrastructure Plan/Design was delayed and has not been completed.</p>	

**Solution Design and Configuration: Observation, Risk, Issue and Feedback/Mitigation****Feedback/Mitigation/Updates**

It is recommended that LSI complete the deliverable as soon as possible.

11/18/2021: LSI submitted Technical Infrastructure Plan/Design and DED for DOTH's review. DOTH requested a revision due to the document being incomplete and inaccurate.

12/2/2021: No major updates.

**Solution Design and Configuration: Observation, Risk, Issue and Feedback/Mitigation****Issue****Impact****ORI ID: R-211118-01**

The consultants do not seem to have experience of FHWA with many appropriations and with front-end split. These are unique requirements that Hawaii DOTH have that adds to the difficulty of the project for the consultants to understand the process and design the solution. Some consultants have very limited experience in those fields and it amplifies the difficulty. Some explore sessions showed that there are still areas that require better understanding of the processes.

**Feedback/Mitigation/Updates**

There may need to be more sessions for a better and full understanding of the FHWA Billing, front-end split, waterfall funding, many-to-many relationship with appropriations and projects, along with any other module or area that need more information for PDD.

The H4 Project Team should ensure the implementation consultants meet the qualifications discussed in the RFP.

12/2/2021: No major updates.

**H. Subject Category: Interface and Integration****Interface and Integration: Observation, Risk, Issue and Feedback/Mitigation****Issue****Impact****ORI ID: I-211028-05**

The Interface Plan was delayed and has not been completed.

**Feedback/Mitigation/ Updates**


It is recommended that LSI complete the deliverable as soon as possible.

11/18/2021: No major updates.


11/24/2021: LSI submitted and DOTH is reviewing it.

12/2/2021: DOTH requested a revision.


## I. Subject Category: Reports and Analytics

Reports and Analytics: Observation, Risk, Issue and Feedback/Mitigation	
Issue	Impact
<b>ORI ID: I-211028-01</b> The Analysis of Reporting Requirements was delayed and has not been completed.	
Feedback/Mitigation/ Updates	
It is recommended that LSI complete the deliverable as soon as possible. 11/18/2021: No major updates. 12/2/2021: No major updates.	

## J. Subject Category: Data Conversion

Data Conversion: Observation, Risk, Issue and Feedback/Mitigation	
Issue	Impact
<b>ORI ID: I-211028-06</b> The Data Conversion Plan was delayed and has not been completed.	
Feedback/Mitigation/ Updates	
It is recommended that LSI complete the deliverable as soon as possible.	

## K. Subject Category: Documentation

Documentation: Observation, Risk, Issue and Feedback/Mitigation	
Issue	Impact
<b>ORI ID: I-211014-02</b> Action items in "Open Items Tracker.xlsx" are not monitored or followed up as often as they should be. The last update date of this document was 8/23/2021 as of 10/15/2021.	
Feedback/Mitigation/ Updates	
Open action items list needs to be updated and monitored regularly in a timely manner and followed through completely and consistently as part of the ongoing project management.	

**Documentation: Observation, Risk, Issue and Feedback/Mitigation**

10/31/2021: No updates. Action items for both LSI and DOTH should be logged with deadline and they need follow ups.

11/18/2021: No major updates.

12/2/2021: No major updates. It is difficult to get a accurate picture of open items.

## L. Subject Category: Training and Knowledge Transfer

**Training and Knowledge Transfer: Observation, Risk, Issue and Feedback/Mitigation****Issue****Impact****ORI ID: I-211028-03**

The End User Training Strategy was delayed and has not been completed.

**Feedback/Mitigation/Updates**

It is recommended that LSI complete the deliverable as soon as possible.

11/2/2021: LSI submitted End User Training Strategy and DOTH's review is being in progress.

12/2/2021: DOTH review is being in progress.

**Training and Knowledge Transfer: Observation, Risk, Issue and Feedback/Mitigation****Observation****ORI ID: O-211028-03**

DOTH project team members are not familiar with H4 system functions and features for PDD review and having difficulty applying them to DOTH's requirements.


**Feedback/Mitigation/Updates**

It is recommended that DOTH project team members request DOTH-specific one-on-one, hands-on training and question and answer sessions for more familiarity with H4 because the project team training conducted by LSI in May 2021 was based on generic and high-level non-DOTH specific requirements without much detail, nor live system demo with exercises.

11/18/2021: No requests for trainings have been made. Training for the project team members should be conducted as soon as possible.

12/2/2021: No major updates.

## M. Subject Category: Production Migration

Production Migration: Observation, Risk, Issue and Feedback/Mitigation	
Issue	Impact
<b>ORI ID: I-211028-07</b> The Initial Deployment Plan was delayed and has not been completed.	
Feedback/Mitigation/ Updates	
It is recommended that LSI complete the deliverable as soon as possible. 11/18/2021: No major updates. 12/2/2021: No major updates.	

## IV. Meetings and Discussions Participated for the Month of November 2021

Meetings and Discussions			
Meeting ID	Meeting Date	Meeting Title	Meeting Description
M211101-1	11/1/2021	FM PDD	A meeting was held to review FM PDD.
M211101-2	11/1/2021	Discuss encumbrance of POs at year-end vs at PO creation (Teams)	A meeting was held to review how often H4 will interface to DAGS.
M211102-1	11/2/2021	Status of Data Conversion	A meeting was held to review and check the status of data conversion items.
M211102-2	11/2/2021	Logistics Process Design Review - MRP	A meeting was held to review Logistics Process Design Review - MRP.
M211103-1	11/3/2021	Analysis of Implementing DMR on SAP PM or AS/400 (Teams)	A meeting was held to discuss and make a decision on whether or not to implement Plant Maintenance module.
M211103-2	11/3/2021	Logistics Process Design Review - Pcard (Teams)	A meeting was held to review Pcard PDD.
M211104-1	11/4/2021	H4 SAP Project Bi-Weekly Meetings	A meeting was held to discuss about interface between SAP and FAMIS.
M211104-2	11/4/2021	LSI Weekly Project Status Meeting	LSI Weekly Project Status meeting was held to report project management status, key milestones, high-level activities, and deliverable status.
M211104-3	11/4/2021	Payroll PDD	A meeting was held to review Payroll PDD.
M211104-4	11/4/2021	Internal debrief on DAGS/ETS interface call	A meeting was held to review interface decision between H4 and DAGS. DOTH is trying to find a way to download data from DataMart.
M211105-1	11/5/2021	FHWA cross-functional workshop (5th Floor Conf room)	A meeting was held to review and discuss FHWA requirements and processes.
M211108-1	11/8/2021	Review PDD FM Budget Execution for CIP-O&M-SMP (Teams)	A meeting was held to review FM PDD.
M211108-2	11/8/2021	HWY-VC Grants	A meeting was held to discuss Motor Carrier Safety Assistance Program (MCSAP).
M211109-1	11/9/2021	Logistics Processing Design Review - Vendor Master (Teams)	A meeting was held to review vendor master PDD.
M211109-2	11/9/2021	HCM PDD Review (Teams)	A meeting was held to review HCM PDD.
M211110-1	11/10/2021	MCSAP Invoice Payment & Cash Receipt Business Processes	A meeting was held to review and discuss MCSAP process.
M211110-2	11/10/2021	AR Playback	A meeting was held to discuss AR process and requirements.
M211110-3	11/10/2021	Overview discussion of Districts' AS/400 functionality (Teams)	A meeting was held to review Districts' AS/400 functions and discuss requirements.
M211110-4	11/10/2021	Explore possible Datamart interface to SAP (Teams call)	A meeting was held to find out feasibility of inbound interface from DataMart to H4.



Meetings and Discussions			
Meeting ID	Meeting Date	Meeting Title	Meeting Description
M211112-1	11/12/2021	LSI Weekly Project Status Meeting	LSI Weekly Project Status meeting was held to report project management status, key milestones, high-level activities, and deliverable status.
M211115-1	11/15/2021	FHWA Earned and unbilled (5th floor conf room)	AR meeting was held to discuss earned and unbilled: Data flow/diagram among FM, PS, FHWA Billing, Pre Split, Post Split, Pre Posting, and After Posting.
M211115-2	11/15/2021	Motor pool works, Warehouse stock and issues, Manual Workorders (5th floor conf room), Complaint data base/ Notifications	A meeting was held to discuss processes of motor pool, warehouse stock, issue, work orders, and complaint database.
M211116-1	11/16/2021	Fixed Assets Master Data & Asset Acquisition Transactions and Closing PDD Review (5th floor conf room)	A meeting was held to review FA PDD.
M211117-1	11/17/2021	FHWA business scenarios (5th floor conf room)	Explore workshop was held to review different types of FHWA business cases.
M211117-2	11/17/2021	Time entry and DMR approvals, Gas and Oil services provided, Safety Permits, FuelMaster (5th Floor conf room)	Explore workshop was held to review processes of DMR, Gas/Oil, permits, FuelMaster, etc.
M211118-1	11/18/2021	LSI Weekly Project Status Meeting	LSI Weekly Project Status meeting was held to report project management status, key milestones, high-level activities, and deliverable status.
M211118-2	11/18/2021	Review AR Process Design Documents ( 5th floor conf room)	A meeting was to held to review AR PDD.
M211118-3	11/18/2021	Purchasing Design (5th floor conf room)	A meeting was held to review and discuss tax, commodity code, and PO hierarchy.
M211119-1	11/19/2021	Review Process Design for MVSO-NHTSA Grants Mgt.	A meeting was held to review MVSO-NHTSA PDD.
M211119-2	11/19/2021	DOT Highways HIP Interface Kickoff	A meeting was held to discuss HIP interface, timeline, and specification.
M211119-3	11/19/2021	AVC Check for Quarterly Budget with GR/IR Invoice Activated	A meeting was held to discuss PO encumbrance liquidation and invoice charging.
M211119-4	11/19/2021	Internal meeting to review updated COA & MDD deliverable for approval (Teams)	A meeting was held to discuss HCOA.
M211122-1	11/22/2021	Continued FA Master Data & Asset Acquisition Transactions and Closing PDD Review (Teams)	A meeting was held to review FA PDD: Master Data, Asset Acquisition Transactions, and Closing.
M211122-2	11/22/2021	Continued - Review Process Design for MVSO-NHTSA Grants Mgt.	A meeting was held to review MVSO-NHTSA PDD: Sponsored Class, Sponsored Program, Grant Master Data, Wire Reimbursement, Expenditure Reimbursement.

## Section: Meetings and Discussions Participated for the Month of November 2021

Meetings and Discussions			
Meeting ID	Meeting Date	Meeting Title	Meeting Description
M211123-1	11/23/2021	Review Finance Design Documents (Teams)	A meeting was held to review Finance PDD: Controlling Data, Park & Post JVs, and Recurring Journals.
M211123-2	11/23/2021	Discuss FHWA Splitting Table and Exit (Teams)	LSI presented FHWA Split process and discovered more requirements.
M211123-3	11/23/2021	Internal debrief on FHWA split meeting (Teams)	Internal debrief meeting was held to discuss follow up action items.
M211124-1	11/24/2021	HIP Interface Meeting Debrief (Teams)	HIP Interface Debrief was held to discuss follow up action items.
M211124-2	11/24/2021	Functional Spec Review for FM-E005_Fund Master Data Attributes	Functional Spec meeting was held to review FM master data attributes such as
M211124-3	11/24/2021	Review project work plan (Teams)	Workshop was held to update and fix project plan.
M211129-1	11/29/2021	Discuss FHWA consultant's email regarding Funds Check	Internal meeting was held to discuss FHWA consultant's email regarding Funds Check.
M211130-1	11/30/2021	Internal prep for COA meeting with LSI (Teams)	Internal meeting was held to prepare for COA meeting with LSI.
M211130-2	11/30/2021	Discuss H4 COA Design (Teams)	A meeting was held to discuss and review H4 COA PDD. DOTH and LSI agreed that the proposed COA will be revised and corrected.
M211130-3	11/30/2021	Continued - Review Finance Design Documents (Teams)	A meeting was held to review Finance PDD: Internal Orders and Recurring Journals.

## V. IV&V Deliverables, Reports and Meetings Completed

IV&V Deliverables, Reports and Meetings Completed					
IV&V ID	IV&V Deliverable Name	LSI Deliverable Name	LSI Wave / Seq ID	Submission Date	Note
IVV1.0	IV&V Management Plan	N/A	N/A	4/20/2021	
IVV2.0	IV&V Project Schedule	N/A	N/A	4/20/2021	
IVV5.0	Verification and Validation of Project Deliverables – Issue and Risk Management Strategy	Issue and Risk Management Strategy	Wave 1 / #5, #6	4/24/2021	
IVV3.01	IV&V Mid-Month Assessment (May 2021)	N/A	N/A	5/14/2021	
IVV4.01	Monthly Project Assessment Report (May 2021)	N/A	N/A	6/3/2021	
IVV5.01	Verification and Validation of Project Deliverables – Project Charter	Project Charter	Wave 1 / #2	6/2/2021	
IVV3.02	IV&V Mid-Month Assessment (June 2021)	N/A	N/A	6/17/2021	
IVV4.02	Monthly Project Assessment Report (June 2021)	N/A	N/A	7/11/2021	
IVV3.03	IV&V Mid-Month Assessment (July 2021)	N/A	N/A	8/2/2021	
IVV4.03	Monthly Project Assessment Report (July 2021)	N/A	N/A	8/13/2021	
IVV3.04	IV&V Mid-Month Assessment (Aug 2021)	N/A	N/A	9/5/2021	
IVV4.04	Monthly Project Assessment Report (Aug 2021)	N/A	N/A	9/21/2021	
IVV3.05	IV&V Mid-Month Assessment (Sep 2021)	N/A	N/A	10/2/2021	
IVV5.03	Verification and Validation of Project Deliverables - Business Process Organizational Change Management (OCM) Plan	Business Process Organizational Change Management (OCM) Plan	Wave 1 / #12	10/6/2021	
IVV5.05	Verification and Validation of Project Deliverables - Communication Plan	Communication Plan	Wave 1 / #8	10/6/2021	
IVV4.05	Monthly Project Assessment Report (Sep 2021)	N/A	N/A	10/9/2021	
IVV3.06	Mid-Month Assessment (Oct 2021)	N/A	N/A	10/19/2021	
IVV5.06	Verification and Validation of Project Deliverables - Chart of Accounts Design	Chart of Accounts Design	Wave 1 / #11	10/25/2021	
IVV5.08	Verification and Validation of Project Deliverables - Enterprise Structure Design Documents	Enterprise Structure Design Documents	Wave 1 / #17	10/27/2021	
IVV4.06	Monthly Project Assessment Report (Oct 2021)	N/A	N/A	11/8/2021	
IVV5.07	Verification and Validation of Project Deliverables - Master Data Design Documents	Master Data Design Documents	Wave 1 / #18	11/8/2021	
IVV3.07	Mid-Month Assessment (Nov 2021)	N/A	N/A	11/30/2021	
IVV5.15	Verification and Validation of Project Deliverables - Interface Plan	Interface Plan	Wave 1 / #21	12/2/2021	
IVV4.07	Monthly Project Assessment Report (Nov 2021)	N/A	N/A	12/17/2021	






### Section: IV&V Deliverables, Reports and Meetings Completed

## VI. IV&V Deliverables, Reports and Meetings Planned To be Completed in Explore Phase

IV&V Deliverables, Reports, Meetings Planned To Be Completed in Explorer Phase					
IV&V ID	IV&V Deliverable Name	LSI Deliverable Name	LSI Wave / Seq ID	Estimated / Submission Date	Note (12/02/2021)
IVV5.04	Verification and Validation of Project Deliverables - Project Management Plan	Project Management Plan	Wave 1 / #3	Dec 2021	Some documents were submitted, and a revision was requested.
IVV5.09	Verification and Validation of Project Deliverables - Data Conversion Plan	Data Conversion Plan	Wave 1 / #22	Dec 2021	
IVV5.10	Verification and Validation of Project Deliverables - Initial Deployment Plan	Initial Deployment Plan	Wave 1 / #23	Dec 2021	
IVV5.11	Verification and Validation of Project Deliverables - Analysis of Reporting Requirements	Analysis of Reporting Requirements	Wave 1 / #15	Dec 2021	
IVV5.12	Verification and Validation of Project Deliverables - Requirements Traceability Matrix	Requirements Traceability Matrix	Wave 1 / #16	Dec 2021	
IVV5.13	Verification and Validation of Project Deliverables - End User Training Strategy	End User Training Strategy	Wave 1 / #19	Dec 2021	
IVV5.14	Verification and Validation of Project Deliverables - Process Design Documents (PDD) (Documented Business Process Model)	Process Design Documents (PDD) (Documented Business Process Model)	Wave 1 / #20	Dec 2021	There are 40 PDD documents planned and some are submitted.
IVV5.16	Verification and Validation of Project Deliverables - Technical Infrastructure Plan/Design	Technical Infrastructure Plan/Design	Wave 1 / #24	Dec 2021	
IVV5.17	Verification and Validation of Project Deliverables - Document Fit/Gap Analysis	Document Fit/Gap Analysis	Wave 1 / #25	Dec 2021	

## VII. Appendix

### A. Impact Definition

Value	Legend	Description
N/A		Not Applicable
No Impact		No Impact
Low		A priority of <b>Low</b> is assigned if there is a possibility of low impact to product quality, scope, cost, and/or schedule. Minimal disruption is possible and some monitoring is likely needed to ensure priority does not increase.
Medium		A priority of <b>Medium</b> is assigned if there is a possibility of moderate impact to product quality, scope, cost, and/or schedule. Some disruption is likely and a different approach may be required. Mitigation strategies should be implemented as soon as feasible.
High		A priority of <b>High</b> is assigned if there is a possibility of substantial impact to product quality, scope, cost, and/or schedule. A major disruption is likely and the consequences would be unacceptable. A different approach is required. Mitigation strategies should be evaluated and acted upon immediately.

### B. Status Definition

Status	Description
Open	Observation, risk, or issue is created.
In Progress	Observation, risk, or issue is addressed and is being worked on by the implementation team.
In Dispute	Observation, risk, or issue is not acknowledged or accepted by the implementation team.
Risk Accepted	Observation, risk, or issue is acknowledged or accepted by implementation team but is not being worked on now.
Closed	Observation, risk, or issue is closed.

## C. Subject Category Definition

Subject	Subject Category	Description
Project Management	Schedule Management	Identify and assess risks and issues that may impact the project completion schedule. This may include analysis of the scale and complexity required, work breakdown and assignments, and assessment of proper planning regarding scope, budget, resources, etc.
	Resource Management	Identify and assess risks and issues associated with allocating proper resources necessary to complete the project.
	Quality Management	Identify and assess risks and issues to quality, specifically software, functionality, testing, documents, etc. via implementation of internal and external measures and processes established to regulate quality level as needed.
	Risk/Issue Management	Identify and assess risks and issues to software and deliverables. This may include considering and/or implementing processes to identify, monitor, communicate regarding, and mitigate potential items that could negatively impact the project.
	Organization Change Management	Identify and assess risks and issues involved in implementing changes necessary to optimize benefits of the new system. This may include end-user education, business process flow, procedures, roles, responsibilities, technology, etc.
	Communication Management	Identify and assess risks and issues that prevent stakeholders from communicating effectively by assessing their key objectives, developing, and implementing procedures to communicate purposes clearly, and analyzing methods to obtain feedback.
	Contract Management	Identify and assess risks and issues that could impact the project team's ability to deliver on its contractual commitments such as cost, scope, size, etc.
	External Impact Management	Identify and assess risks and issues external to DOTH, IV&V, and LSI that could impact the following: subcontractors, regulatory, market, customer, weather, etc.
Implementation	Requirement Management (Processes, Requirements and Fit/Gap)	Identify and assess risks and issues to business process, system software requirements, and fit/gap of process and available functionalities of the software.
	Solution Design and Configuration	Identify and assess risks and issues to solution design and configuration of the software implementation of the system.
	Interface and Integration	Identify and assess risks and issues that relate to functionalities that interact with outside system or software.
	Reports and Analytics	Identify and assess risks and issues to reporting and analytics functionality of the system.
	Security	Identify and assess risks and issues to security of the system such as authentication, user access control, encryption, or any other items that relate to keeping the information secure.
	Data Conversion	Identify and assess risks and issues to data conversion process or resulting data when moving data from the old system to the new system.

Subject	Subject Category	Description
	Documentation	Identify and assess risks and issues in documentation deliverables.
	System Testing	Identify and assess risks and issues related to testing the functionalities of the system for the requirements.
	Training and Knowledge Transfer	Identify and assess risks and issues with training and knowledge transfer of the new system and its use.
	Production Migration	Identify and assess risks and issues to the system migrating from test environment to production environment.

D. Observation, Risk, and Issues List



Observation, Risk and Issues (ORI) 12/2/2021																	
ORI ID	Type	LSI Deliverable / ORI Source	Creation Date	Subject Area	Modules	Summary	Description	Responsible Party	Status	Impact	Probability	Feedback / Mitigation	Updates	Review / Target Date	Close Date	Reference ID/Doc	Comments
O-210330-01	Observation	M210330-1	3/30/2021	Schedule Management	N/A	Aggressive Project Plan and Go Live Date	The Prepare Phase was started in March 2021. The major activities in the Prepare Phase are the Project Charter, the Project Plan, the Communication Plan, the Project Team Training Plan, the Project Team Training, the COA Design Workshop, the Organization Change Management Plan, and the ENV Preparation. After completion of the Prepare Phase, starting the Explore phase in June leaves only 13 months to Go-Live and this can be an aggressive project plan.	DOH/LSI	Closed	N/A	N/A	PMO and IV&V should check and monitor project status and activities to ensure the project is on schedule. June is the busiest month for DOTH preparing for Fiscal Year end and LSI should be cognizant of it when scheduling the Explore Phase tasks.		6/30/2021	6/30/2021		
O-210407-01	Observation	Email-Ron-210407	4/7/2021	Resource Management	N/A	Replacement of LSI Project Manager	The project manager, Matthew was replaced by John on 4/7/2021. Matthew was involved in contract scope of work, project plan and discussions with DOTH until he left LSI.	LSI	Closed	N/A	N/A	PMO and IV&V should check and monitor if there's a smooth transition in roles and responsibility of LSI PM.		5/31/2021	5/31/2021		
O-210429-01	Observation	M210429-1	4/29/2021	Resource Management	N/A	In progress of identifying LSI Organization Change Management Lead	LSI is currently trying to secure an Organization Change Management Lead personnel.	LSI	Closed	N/A	N/A	PMO and IV&V should check and monitor to ensure LSI brings the Organization Change Management Lead into the project as soon as possible according to the staffing plan (June).	7/1/2021: Organization Change Management Lead will join the implementation team on 7/6/2021.	6/30/2021	6/30/2021		
O-210429-02	Observation	M210429-1	4/29/2021	Schedule Management	N/A	Updating LSI project plan	LSI is currently updating project plan with correct date and resource assignment. "Updated Project Plan and Implementation Schedule" was returned to LSI for more completed document with updates to dates and resource assignment, etc.	LSI	Closed	N/A	N/A	PMO and IV&V should check and monitor LSI project plan updates.	5/14/2021: IV&V Mid Month Meeting: IV&V and DOTH agreed that the project plan should be delivered as soon as possible for project management and schedule. Per meeting, expected updated Project Plan delivery date is 5/21/2021. 5/28/2021: This observation became an issue.	5/31/2021	5/31/2021	I-210531-02	
O-210505-01	Observation	M210504-1	5/5/2021	Contract Management	N/A	FMS Kick Off Meeting	Kick Off meeting was held on 5/5/2021 and the presentation was well organized and delivered nicely.	LSI	Closed	N/A	N/A	N/A		5/31/2021	5/31/2021		
O-210505-02	Observation	M210504-2	5/5/2021	Training and Knowledge Transfer	GL	SAP S/4 ERP Essential Concepts for the DOTH FMS	Overall training went well, however there were some people who couldn't log in and were not able to follow the training and that was not addressed during the training. There also were some minor technical difficulty with switching screen (or may have been switching between presentation decks).	DOH/LSI	Closed	N/A	N/A	There needs to be a process in place where participants are monitored for questions or issues during training. There may need some general training for MS teams presentation (including meeting settings setup, monitoring participants, sharing screen, muting/unmuting participants) usage.		5/31/2021	5/31/2021		
O-210505-03	Observation	M210505-1	5/5/2021	Resource Management	PG	Retirement of HYWAC Resource in Dec 2021	A key DOTH personnel, Chuck for HYWAC will retire in Dec 2021.	DOH	Closed	N/A	N/A	DOH should ensure to have a proper knowledge transfer and transition to his successor. DOTH already hired another employee and she's getting trained and prepared to be responsible for HYWAC maintenance and support.		5/31/2021	5/31/2021		
O-210512-01	Observation	M210512-2	5/12/2021	Training and Knowledge Transfer	N/A	Generic Training without focus of DOTH requirements	Project Team Training were conducted by LSI based on generic functionalities of SAP. However, LSI's proposal stated "Functional project team training will take place as a Explore activity, and will be delivered by LSI functional consultants. This is a differentiator, because the training is not centered on a generic system with a universe of capabilities, but will be focused on DOTH's system functionality as delivered"	LSI	Closed	N/A	N/A	LSI project manager stated that there would be more Discovery Workshop that will review and discuss DOTH's specific requirements and learn how SAP's functionalities will meet DOTH's requirements. It needs to be confirmed in which deliverable that these workshop will be performed in the plan.		5/31/2021	5/31/2021		
O-210513-01	Observation	M210513-1	5/13/2021	Resource Management	N/A	In progress of identifying LSI Payroll/HR/Time & Attendance Lead	LSI is currently trying to secure a LSI Payroll/HR/Time & Attendance Lead.	LSI	Closed	N/A	N/A	The Payroll/HR/Time & Labor Leads are currently not identified and PMO and IV&V should check and monitor to ensure LSI brings resources into the project by July according to the staffing plan.		7/31/2021	7/31/2021		
O-210513-02	Observation	Email-Ron-20210513	5/13/2021	Schedule Management	N/A	Project Team Training Plan document hasn't submitted by LSI.	Project Team Training (LSI Wave1/Seq ID: 9) was started without Project Team Training Plan Document submitted to DOTH (LSI Wave1/Seq ID: 10).	LSI	Closed	N/A	N/A	PMO and IV&V should check and monitor to ensure LSI delivers Team Training Plan Document (LSI Wave1/Seq ID: 10).	DOH and LSI agreed to skip the training plan since LSI conducted the Project Team Training already.	5/31/2021	5/31/2021	O-210617-01	
O-210514-01	Observation	M210514-2	5/14/2021	Training and Knowledge Transfer	N/A	SAP Terminology	DOTH project team members stated that during the SAP project team training (Introduction to SAP), DOTH project team members had difficulty understanding SAP's terminology and relating SAP's terminology and standard functions to DOTH's requirements. The introduction to SAP training was mostly centered around SAP standard functionality and did not strongly correlate to DOTH's requirements.	DOH/LSI	Closed	N/A	N/A	LSI consultants need to learn and be more familiar with DOTH's business requirements along with DOTH's terminology and processes as listed in RFP and LSI's proposal. Also DOTH project team members should learn and be more familiar with SAP terminologies as well. LSI should start to dive into DOTH's requirements and conduct the training with DOTH's specific requirements, not only generic SAP standard functions. Cross reference of terminology (SAP & DOTH terminology glossary) would help DOTH project team members to understand how SAP functionality will work for DOTH's requirements.		5/31/2021	5/31/2021		
O-210514-02	Observation	M210520-1	5/14/2021	Resource Management	N/A	DOTH Project Team Availability	DOTH project team members stated that June through September are the busiest months of the year and expressed concerns on project participation. Fiscal (HWY-SF) is the busiest in June and July, Budget (HWY-SB) is the busiest in September and October, and Project/Grants (HWY-SM) is the busiest in August and September. Each department of DOTH has particularly busy times in a year, but not all at the same time.	DOH/LSI	Closed	N/A	N/A	LSI and DOTH should determine the busy season of the year and the availabilities of SMEs to schedule the meetings around those availabilities of SMEs for efficient and effective use of meeting time without impacting DOTH's regular business activity. DOTH is waiting for the Project Plan so that DOTH can schedule their time accordingly.		6/30/2021	6/30/2021		

Observation, Risk and Issues (ORI) 12/2/2021																	
ORI ID	Type	LSI Deliverable / ORI Source	Creation Date	Subject Area	Modules	Summary	Description	Responsible Party	Status	Impact	Probability	Feedback / Mitigation	Updates	Review / Target Date	Close Date	Reference ID/Doc	Comments
O-210527-01	Observation	Email-Ron-210527	5/27/2021	Quality Management	N/A	SAP Support Website	DOTH purchased SAP software license. As of 5/26, there is no established account and access for SAP support website. IV&V brought up that DOTH purchased software licenses and that they should be provided access to the SAP support website that including product information, troubleshooting and direct SAP support.	LSI	Closed	N/A	N/A	It is recommended that LSI support and follow up with SAP for DOTH to gain access to the SAP support website.	9/2/2021: As of 9/2/2021, there is no established account and access for SAP support website. LSI stated that it will be available after Development environment is installed. 9/8/2021: LSI provided DOTH with access to SAP support website.	9/16/2021	9/16/2021	O-210923-01	
I-210531-01	Issue	M210527-1	5/31/2021	Schedule Management	N/A	Delay in Deliverables	As of 5/31/2021, the deliverables of the Communication Plan, the Chart of Accounts Design, the Business Process Organizational Change Management (OCM) Plan, the Project Management Plan (PMP) and the Project Team Training have not been submitted to DOTH or completed yet. They were due on or prior to 5/31/2021, which was the end of the Prepare Phase.	LSI	Closed	Low	N/A	LSI should complete the Communication Plan, the Chart of Accounts Design, the Business Process Organizational Change Management (OCM) Plan, and the Project Management Plan and submit to DOTH for review as soon as possible.	6/3/2021: The New Target Dates for the following deliverables are set to by LSI: - Communication Plan: 6/11/2021 - Chart of Accounts Design: 7/2/2021 - Business Process Organizational Change Management (OCM) Plan: 6/11/2021 - Project Management Plan (PMP): 6/18/2021 - Project Team Training: 6/18/2021	6/30/2021	6/30/2021	O-210615-01	Closed and recreated as I-210615-01
I-210531-02	Issue	M210527-1	5/31/2021	Schedule Management	N/A	Project Plan and Implementation Schedule	The final Project Plan/Implementation Schedule has not been completed and submitted to DOTH. This is a foundational document for a project management and scheduling and one of the most critical deliverables. Delay in the Project Plan and implementation Schedule pose decreased confidence in being able to meet the final Go-Live date. Also, without the Project Plan and the Implementation Schedule DOTH has limited project visibility and it will impact schedule and resource management.	LSI	In Progress	High	N/A	LSI should complete Project Plan/Implementation Schedule as soon as possible.	6/3/2021: The New Target Date for Project Plan/Implementation Schedule is set to 6/11/21 by LSI. 6/14/2021: Updated project plan was submitted by LSI but returned back to LSI due to incompleteness. 7/1/2021: It is currently unknown, at a detail level, if the number of resources are adequate to complete the project on schedule. Earlier versions of the Project Plan were not accepted partly because of oversubscribed resources and incorrect dates (i.e. one consultant or DOTH team member working more than 40 hours in a week, etc.) - 11/16/2020: The initial project plan was submitted and returned back to LSI after DOTH review due to incompleteness. - 12/21/2020: Updated project plan was submitted by LSI but returned back to LSI after DOTH review due to incompleteness. - 4/26/2021: Updated project plan was submitted by LSI but returned back to LSI after DOTH review due to incompleteness. - 6/14/2021: Updated project plan was submitted by LSI but returned back to LSI after DOTH review due to incompleteness. - 7/1/2021: Updated project plan was submitted by LSI but returned back to LSI after DOTH review due to incompleteness. Revised Acceptance Date: 8/31/2021 9/02/2021: No updates have been submitted to DOTH. 9/16/2021: DOTH interviewed an assistant project manager candidate on 9/7/2021. 9/30/2021: No updates have been submitted to DOTH. 10/5/2021: LSI Assistant Project Manager submitted the revised project plan. DOTH has a meeting with the LSI	12/2/2021			
O-210610-01	Observation	M210610-1	6/10/2021	Schedule Management	N/A	Explore Workshop - Schedule	The Explore As-Is on-site workshops are scheduled for three hours each to cover one or two business areas. These sessions might not be enough time for thorough review and discussion. No on-site or off-site sessions are scheduled for Thursday afternoons and Fridays even though DOTH staff is available and contractors are expected to be available for work during DOTH business hours.	LSI	Closed	N/A	N/A	LSI and DOTH should facilitate and run workshops effectively to cover all the processes with sufficient details within the allotted time. LSI may need to engage during DOTH working hours including Thursday afternoon and Friday based on project needs, especially for on-site or off-site workshops since DOTH staff is available during those times.		6/30/2021	6/30/2021		
O-210610-02	Observation	M210610-1	6/10/2021	Schedule Management	N/A	Start Date of Explore Workshop	The Explore Workshop that includes As-Is, To-Be, Requirements Analysis are scheduled to start on 6/21/2021. June is the last month of a Fiscal Year and it is the busiest month of the year and last couple weeks of June are the busiest weeks of the year. Ideally, June should have been avoided for DOTH time consuming activities. If these activities had to be scheduled in June, it could have at least started in the first week of June when SMEs were less busier than latter part of June. It was observed that DOTH staff was not able to fully focus on the Explore Workshop due to legislative deadline that DOTH had to meet for the fiscal year end.	LSI	Closed	N/A	N/A	PMO should check and monitor project scheduling where DOTH personnel are required to ensure that disruption to DOTH's daily task is minimized. June is the busiest month for DOTH preparing for Fiscal Year end and LSI should be cognizant of DOTH's busy times when scheduling the DOTH time consuming tasks.		7/31/2021	7/31/2021		
O-210610-03	Observation	M210610-1	6/10/2021	Solution Design and Configuration	N/A	VPN Connection	VPN connection between LSI AWS and DOTH is being established and tested. It should thoroughly reviewed and tested for compatibility with the State network to ensure all expected features are functioning properly, including what steps are required for users to activate VPN to access SAP, how SAP sends print jobs to DOTH printers in the state network, etc.	LSI	Closed	N/A	N/A	N/A		7/31/2021	7/31/2021		
O-210610-4	Observation	M210610-1	6/10/2021	Schedule Management	N/A	SAP Standard Process	DOTH expressed concerns about overall progress of the project. The concerns included not starting DOTH's requirements analysis in the beginning of the Explore Phase and not starting SAP standard processes analysis and fit/gap analysis earlier.	LSI	Closed	N/A	N/A	N/A		7/31/2021	7/31/2021		

Observation, Risk and Issues (ORI) 12/2/2021																	
ORI ID	Type	LSI Deliverable / ORI Source	Creation Date	Subject Area	Modules	Summary	Description	Responsible Party	Status	Impact	Probability	Feedback / Mitigation	Updates	Review / Target Date	Close Date	Reference ID/Doc	Comments
I-210615-01	Issue	DOTH FMS Change Request Form #1	6/15/2021	Schedule Management	N/A	Delay in Deliverables	LSI requested a change request and DOTH approved it. The completion of following deliverables will be delayed until the Explore Phase. #3 Project Management Plan #7 Updated Project Plan and Implementation Schedule #8 Communication Plan #9 Project Team Training Plan #10 Project Team Training #11 Chart of Accounts Design #12 Business Process Organization Change Management (OCM) Plan	LSI	Closed	Low	N/A	It is recommended that LSI complete these deliverables and submit to DOTH for review as soon as possible. As these deliverables are postponed to the Explore Phase, workload in the Explore Phase has been increased. The Implementation Team needs to monitor the Explore Phase to ensure on time completion of the deliverables to minimize and eliminate potential risks with timeline due to more deliverables and more workload in the Explore Phase.	7/1/2021: - Communication Plan: Submitted 6/15/21 for DOTH's review. DOTH reviewed and found a few issues. - Chart of Accounts Design: Target date =7/2/2021 - Business Process Organizational Change Management (OCM) Plan: Submitted 6/15/21 for DOTH's review. - Project Management Plan (PMP): Target Date=TBD. Strategy documents are being worked on. - Project Team Training: Target Date=TBD 7/31/2021: #3 Project Management Plan: See I-210630-01. #7 Updated Project Plan and Implementation Schedule: See I-210531-02. #8 Communication Plan: TBD #9 Project Team Training Plan: TBD #10 Project Team Training: TBD #11 Chart of Accounts Design: TBD #12 Business Process Organization Change Management (OCM) Plan: TBD 9/2/2021: No changes. 9/16/2021: No changes. 9/30/2021: Communication Plan and Business Process Organization Change Management (OCM) Plan were submitted and approved by DOTH. Payment was made for Project Team Training. No changes to other documents and the estimated delivery dates are 10/31/2021. 10/15/2021: No changes. 10/31/2021: Chart of Account Design document was submitted and being reviewed by DOTH.	10/31/2021	10/31/2021	I-211028-10	
O-210617-01	Observation	M210617-1	6/17/2021	Schedule Management	N/A	Project Team Training Plan Document	DOTH and LSI agreed to skip the Project Team Training Plan on 5/15/2021 since LSI already conducted the Project Team Training without Project Team Training Plan. However, LSI decided to work on Project Team Training Plan Document (LSI Wave1/Seq ID: 10) and submit to DOTH by June 2021 for review.	LSI	Closed	N/A	N/A	PMO and IV&V should check and monitor to ensure LSI delivers Project Team Training Plan Document (LSI Wave1/Seq ID: 10).	6/17/2021: New Observation, O-210617-01 is created from O-210513-01.	7/31/2021	7/31/2021	O-210513-01	
O-210624-01	Observation	M210624-1	6/24/2021	Resource Management	N/A	DOTH Requirements	During the Explore Workshop (As-Is), it was noticed that LSI consultants may have different levels of expertise and understanding of their respective responsible business areas and general government sector requirements.	LSI	Closed	N/A	N/A	LSI consultants should become familiarize as soon as possible with general DOTH information and requirements that were provided in RFP and other documents.		6/30/2021	6/30/2021		
O-210624-02	Observation	M210621-1	6/24/2021	Communication Management	N/A	Virtual Meeting	During the Explore Workshop (As-Is), there was a technical difficulty with microphone in Teams meeting. The remote participants in Teams had a hard time hearing the meeting discussion.	DOTH	Closed	N/A	N/A	Given the environment where virtual meetings will be common, these type of technical difficulty should be resolved as soon as possible.		6/30/2021	6/30/2021		
O-210624-03	Observation	M210701-1	6/24/2021	Requirement Management (Processes, Requirements and Fit(Gap)	N/A	Updated As-Is	DOTH provided updated As-Is business flows to LSI for individual business area for the Explore Workshop and utilized these business flows to explain DOTH processes and procedures.	DOTH	Closed	N/A	N/A	N/A		6/30/2021	6/30/2021		
O-210624-04	Observation	M210624-1	6/24/2021	Requirement Management (Processes, Requirements and Fit(Gap)	N/A	Explore Workshop	There are some core business processes that are not covered yet in the first Explore Workshops including split cost for federal billing, waterfall funding, link project cos tot specific state appropriation, labor compression, county pass-through and MVSO.	DOTH/LSI	Closed	N/A	N/A	Both DOTH and LSI should proactively convey and explore the As-Is processes to ensure all the business processes are covered for the requirements. There should be a continuation of further exploring and understanding of DOTH business process. It is encouraged that LSI consultants to review requirements in detail to maximize information gathering and to not miss business process areas for the Explore Workshops.		7/31/2021	7/31/2021		Closed and created as DOTH Critical Core Requirements.

Observation, Risk and Issues (ORI) 12/2/2021																	
ORI ID	Type	LSI Deliverable / ORI Source	Creation Date	Subject Area	Modules	Summary	Description	Responsible Party	Status	Impact	Probability	Feedback / Mitigation	Updates	Review / Target Date	Close Date	Reference ID/Doc	Comments
I-210630-01	Issue	DOTH FMS Change Request Form #2	6/30/2021	Schedule Management	N/A	Delay in Deliverables	LSI requested a change request and DOTH approved it. The completion of following deliverables will be delayed until the Explore Phase. #17 Quality Assurance and Testing Strategy #18 Project RACI Strategy #24 Workflow Strategy #25 Reporting Strategy #26 Integration Strategy #27 Conversion Strategy #28 Enhancement Strategy #29 Form Strategy #40 RTMs mapped to Workshops / SAP Modules #53 Preliminary WRICEF Inventory	LSI	Closed	Low	N/A	LSI should complete these deliverables and submit to DOTH for review as soon as possible. As these deliverables are pushed to the Explore Phase, work load in the Explore Phase has been increased and the risk of completion on time in the Explore Phase needs to be properly addressed and monitored.	7/31/2021: #17 Quality Assurance and Testing Strategy: Submitted by LSI on 7/20/2021 and being reviewed by DOTH. #18 Project RACI Strategy: Submitted by LSI on 7/7/2021 and returned to LSI with comments. #24 Workflow Strategy: Submitted by LSI on 7/7/2021 and returned to LSI with comments. #25 Reporting Strategy: Submitted by LSI on 7/7/2021 and returned to LSI with comments. #26 Integration Strategy: TBD. #27 Conversion Strategy: Submitted by LSI on 7/20/2021 and being reviewed by DOTH. #28 Enhancement Strategy: Submitted by LSI on 7/7/2021 and returned to LSI with comments. #29 Form Strategy: Submitted by LSI on 7/7/2021 and returned to LSI with comments. #40 RTMs mapped to Workshops / SAP Modules: TBD #53 Preliminary WRICEF Inventory: TBD 9/2/2021: No changes. 9/16/2021: No changes. 9/30/2021: Conversion Strategy, Enhancement Strategy, Form Strategy, and Workflow Strategy are submitted and approved by DOTH. 10/15/2021: No changes. 10/31/2021: Project RACI Strategy was submitted and approved by DOTH.	10/31/2021	10/31/2021	I-211028-02, I-211028-10	
O-210708-01	Observation	M210708-1	7/8/2021	Resource Management	BD	Replacement of LSI Fund Management Consultant	Fund Management consultant left LSI and LSI brought on a new consultant to DOTH FMS project team.	LSI	Closed	N/A	N/A	N/A		7/31/2021	7/22/2021		
O-210708-03	Observation	M210708-1	7/8/2021	External Impact Management	GL	New UCOA of Statewide Financial System	DOTH FMS is required to be compatible with DAGS's future statewide financial system. However, the new UCOA is still under development at DAGS and the incomplete UCOA at DAGS could cause DOTH some rework after Go-Live.	DOTH/LSI	Closed	N/A	N/A	It is recommended that DOTH and LSI hold a meeting with DAGS to find out future plan and timeline of implementing UCOA. It is also important to obtain latest UCOA contents, changes, updates, etc. compared to the FAMIS account codes.	9/2/2021: A meeting with DAGS was held on 8/12/2021. DOTH and DAGS discussed the new UCOA. Additional meetings need to be scheduled for further discussion and clarification of the new UCOA.	9/2/2021	9/2/2021	R-210812-01	Closed and recreated as R-210812-01
R-210812-01	Risk	M210812-3	8/12/2021	External Impact Management	GL	New UCOA of Statewide Financial System	DOTH FMS is required to be compatible with DAGS's future statewide financial system. A meeting with DAGS was held on 8/12/2021 and DOTH and DAGS discussed the new UCOA. However, the new UCOA is still under development at DAGS and the incomplete UCOA at DAGS could cause DOTH some rework after the new statewide financial system goes live. The implementation project for statewide the financial management system hasn't started yet and Go-Live date has not been determined either.	DOTH/LSI	In Progress	Low	Low	It is recommended that additional meetings need to be scheduled for further discussion and clarification of the new UCOA including the latest UCOA contents, changes, updates, etc. compared to the FAMIS account codes.	9/16/2021: No additional meetings with DAGS were scheduled. 9/30/2021: No updates. 10/15/2021: No updates. 10/31/2021: No updates. 11/18/2021: LSI and DOTH discussed if UCOA is the best fit for DOTH. Another meeting is scheduled on 11/29/2021. 11/30/2021: LSI and DOTH discussed H4 COA and agreed that LSI will perform more analyses and update/fix H4 COA.	12/2/2021			
O-210708-02	Observation	M210708-1	7/8/2021	External Impact Management	GL	Interface with FAMIS	Feasibility of Inbound and outbound FAMIS interfaces need to be discussed with and confirmed by DAGS.	DOTH/LSI	Closed	N/A	N/A	It is recommended that DOTH and LSI hold a meeting with DAGS to find out if DAGS allows DOTH to interface files to FAMIS (DOTH Outbound Interface) and DAGS can interface files to DOTH (DOTH Inbound Interface).	9/2/2021: No meetings or discussions were held. 9/16/2021: No meetings or discussions were held. 9/20/2021: A meeting with ETS was held and found out that GL Interface is not currently available in FAMIS. 10/15/2021: There will be a meeting, but no date has been set. 10/22/2021: LSI and DOTH had a meeting with DAGS to discuss FAMIS interface. 11/4/2021: LSI and DOTH/ETS had a meeting with DAGS to discuss FAMIS interface. ETS confirmed that there is no JV interface and no outbound interface from FAMIS available and no plan to develop it.	11/18/2021	11/18/2021		DOTA receives FAMIS files. It's recommended that the H4 Project Team find more information about possibility of extracting financial data from the FAMIS files in DOTA. Another option for extracting financial data is from DataMart.
I-210722-01	Issue	M210722-1	7/22/2021	Requirement Management (Processes, Requirements and Fit/Gap)	N/A	Explorer Workshop	The Explorer Workshops are conducted from SAP point of view. Consultants are introducing and explaining generic functions and features of SAP products before completing a thorough analysis of DOTH requirements listed in RFP with DOTH project team members. Some of the functional examples or concepts from the Explorer Workshops were too generic or not directly related to DOTH processes and requirements. Therefore, DOTH project team members are having difficult time understanding SAP functionalities and connecting SAP functionalities to DOTH processes and requirements.	LSI	Closed	Low	N/A	It is recommended that LSI hold additional sessions and/or utilize the remaining Explore Workshops to review and confirm the DOTH business terminologies, processes, and requirements to effectively communicate with DOTH and to propose DOTH specific solutions.	7/31/2021: More DOTH requirements have been reviewed and discussed during the Explore workshops. However, DOTH project team members are still having difficulty understanding and connecting SAP functions and features to DOTH requirements. 9/2/2021: There were improvements, but many instances are observed where the DOTH team members were having difficult time understanding the workshops. 9/30/2021: There were continuous improvements, but there are some areas where DOTH team members were having difficult time understanding the workshops. 10/15/2021: No major updates. 10/31/2021: No major updates. There were two Integrated Scenario Playback sessions on Oct 13 and Oct 27 2021. However, DOTH project team expressed they need more training and more DOTH requirements specific demo to better understand SAP.	11/18/2021	11/18/2021		This issue is no longer applicable for the Explore phase.
I-210722-02	Issue	M210722-1	7/22/2021	Resource Management	N/A	LSI Consultants On-Site	LSI core team consultants are currently on-site less than 20%, less than one week per month during Explore Phase, whereas the contract states LSI consultants are supposed to be on-site more than 60%. LSI acknowledged the issue and is taking action for more on-site availability.	LSI	Closed	Low	N/A	N/A	9/2/2021: LSI consultants' on-site availability increased.	9/2/2021	9/2/2021		

Observation, Risk and Issues (ORI) 12/2/2021																	
ORI ID	Type	LSI Deliverable / ORI Source	Creation Date	Subject Area	Modules	Summary	Description	Responsible Party	Status	Impact	Probability	Feedback / Mitigation	Updates	Review / Target Date	Close Date	Reference ID/Doc	Comments
O-210722-01	Observation	M210722-1	7/22/2021	Resource Management	N/A	Assistant Project Manager	Assistant Project Manager was no longer with the project and LSI identified a replacement resource who will join the project soon.	LSI	Closed	N/A	N/A	N/A	9/2/2021: LSI identified an assistant project manger and is in the process of hiring him.	9/2/2021	9/2/2021		
O-210729-08	Observation	M210729-1	7/29/2021	Risk/Issue Management	N/A	Status Rating on Dashboard	Status ratings on Dashboard of Project Status Report are all set to green, however there were two change orders issued to postpone deliverables to the next phase and the project plan is still under development.	LSI	Closed	Low	Low	It is recommended that DOTH discuss with LSI to ensure Dashboard Status are agreed by both parties. (i.e., while the anticipated project Go-Live date hasn't changed, many other deliverables are already delayed)	9/2/2021: DOTH and LSI will coordinate to ensure that they agree on Dashboard Status.	9/2/2021	9/2/2021		
O-210729-01	Observation	M210729-1	7/29/2021	Requirement Management (Processes, Requirements and	N/A	Inventory, Payroll and Plant Maintenance	Some requirements may be directly or indirectly related to inventory, Payroll, and Plant Maintenance modules. However, the typical core requirements of these modules, Inventory, Payroll, and Plant Maintenance were not included in the DOTH RFP	DOTH/LSI	Closed	N/A	N/A	It is recommended that DOTH discuss with LSI and determine the implementation scope of inventory, Payroll and Plant Maintenance modules for 7/1/2022 Go-Live.	9/2/2021:The implementation scope of inventory, Payroll, and Plant Maintenance aren't finalized. DOTH and LSI need to make a decision on which functions/features will be implemented to meet DOTH	10/15/2021	10/15/2021	O-211014-01	
O-210729-02	Observation	M210729-1	7/29/2021	Requirement Management (Processes, Requirements and Fit/Gap)	N/A	DOTH Critical Core Requirement	DOTH critical core requirement, "Split Cost for Federal Billing" started being discussed in Explore Workshops, however there are more details to be covered. Explore is in progress. A high level solution design is scheduled to be developed and confirmed by DOTH in the Explore Phase.	DOTH/LSI	Closed	N/A	N/A	N/A	9/2/2021: No updates were reported to DOTH. 9/14/2021: LSI proposed a solution for the requirement of "Split Cost for Federal Billing". More discussion and review are needed. 9/30/2021: No major updates. 10/15/2021: Infrastructure Type requirement was discussed for the first time during the Scenario Demo, however there was a gap between LSI's understanding and DOTH's requirement for the "Split Cost for Federal Billing" requirement. This highlights the need for better and earlier requirements discussion to correctly understand DOTH's requirements and eliminate any gaps. LSI should continue to make progress with confirming the understanding of the requirement and ensuring the underlying assumption is the correct DOTH business process. 10/31/2021: No major updates.	11/18/2021	11/18/2021	I-211115-01	This observation has been closed and recreated as an issue.
O-210729-03	Observation	M210729-1	7/29/2021	Requirement Management (Processes, Requirements and Fit/Gap)	N/A	DOTH Critical Core Requirement	DOTH critical core requirement, "Waterfall Funding" started being discussed in Explore Workshops, however there are more details to be covered. Explore is in progress. A high level solution design is scheduled to be developed and confirmed by DOTH in the Explore Phase.	DOTH/LSI	Closed	N/A	N/A	N/A	9/2/2021:No updates were reported to DOTH. 9/14/2021: LSI proposed a solution for the requirement of "Waterfall Funding". More discussion and review are needed. 9/30/2021: No major updates. 10/15/2021: Infrastructure Type requirement was discussed for the first time during the Scenario Demo, however there was a gap between LSI's understanding and DOTH's requirement for the "Waterfall Funding" requirement. This highlights the need for better and earlier requirements discussion to correctly understand DOTH's requirements and eliminate any gaps. LSI should continue to make progress with confirming the understanding of the requirement and ensuring the underlying assumption is the correct DOTH business process. 10/31/2021: No major updates.	11/18/2021	11/18/2021	I-211115-01	This observation has been closed and recreated as an issue.
O-210729-04	Observation	M210729-1	7/29/2021	Requirement Management (Processes, Requirements and Fit/Gap)	N/A	DOTH Critical Core Requirement	DOTH critical core requirement, "Link Project Cost to Specific State Appropriation" started being discussed in Explore Workshops, however there are more details to be covered. Explore is in progress. A high level solution design is scheduled to be developed and confirmed by DOTH in the Explore Phase.	DOTH/LSI	In Progress	N/A	N/A	N/A	9/2/2021: No updates were reported to DOTH. 9/30/2021: There were discussions in Explore Workshops and preliminary design is being developed. 10/15/2021: No major updates. 10/31/2021: No major updates. 11/18/2021: Discussions are in progress. No major updates. 12/2/2021: Discussions are in progress. No major updates.	12/2/2021			
O-210729-05	Observation	M210729-1	7/29/2021	Requirement Management (Processes, Requirements and Fit/Gap)	N/A	DOTH Critical Core Requirement	DOTH critical core requirement, "Accounting for Appropriated, Allotted, and Cash Authority" started being discussed in Explore Workshops, however there are more details to be covered. Explore is in progress. A high level solution design is scheduled to be developed and confirmed by DOTH in the Explore Phase.	DOTH/LSI	In Progress	N/A	N/A	N/A	9/2/2021: No updates were reported to DOTH. 9/30/2021: There were discussions in Explore Workshops and preliminary design is being developed. 10/15/2021: Discussions are in progress. No major updates. 10/31/2021: Discussions are in progress. No major updates. 11/18/2021: Discussions are in progress. No major updates. 12/2/2021: Discussions are in progress. No major updates.	12/2/2021			
O-210729-06	Observation	M210729-1	7/29/2021	Requirement Management (Processes, Requirements and Fit/Gap)	N/A	DOTH Critical Core Requirement	DOTH critical core requirement, "Labor "Compression" started being discussed in Explore Workshops, however there are more details to be covered. Explore is in progress. A high level solution design is scheduled to be developed and confirmed by DOTH in the Explore Phase.	DOTH/LSI	In Progress	N/A	N/A	N/A	9/2/2021: No updates were reported to DOTH. 9/30/2021: There were discussions in Explore Workshops and preliminary design is being developed. Payroll interface was discussed in the meeting with ETS on 9/28/2021. 10/15/2021: Discussions are in progress. No major updates. 10/31/2021: Discussions are in progress. No major updates. 11/18/2021: HIP Interface discussions with ETS are in progress. 12/2/2021: Discussions are in progress. No major	12/2/2021			

Observation, Risk and Issues (ORI) 12/2/2021																	
ORI ID	Type	LSI Deliverable / ORI Source	Creation Date	Subject Area	Modules	Summary	Description	Responsible Party	Status	Impact	Probability	Feedback / Mitigation	Updates	Review / Target Date	Close Date	Reference ID/Doc	Comments
O-210729-07	Observation	M210729-1	7/29/2021	Requirement Management (Processes, Requirements and Fit/Gap)	N/A	DOH Critical Core Requirement	DOH critical core requirement. "The State Financial Accounting System" started being discussed in Explore Workshops, however there are more details to be covered. Explore is in progress. A high level solution design is scheduled to be developed and confirmed by DOH in the Explore Phase.	DOH/LSI	In Progress	N/A	N/A	N/A	9/2/2021: No updates were reported to DOH. 9/20/2021: There was a FAMIS interface discussion with ETS. 10/15/2021: Discussions are in progress. No major updates. 10/22/2021: LSI and DOH had a meeting with DAGS to discuss FAMIS interface. Email correspondents were exchanged as follow-up. 11/4/2021: LSI and DOH had a meeting with DAGS and ETS to discuss interface between FAMIS and H4. 11/10/2021: DOH had a meeting with eWorld to discuss possibility of downloading FAMIS data from DataMart. 12/2/2021: No major updates.	12/2/2021			
O-210804-01	Observation	M210804-2	8/4/2021	Resource Management	BD	Participation of Budget and Planning Consultant	Budget and Planning module in Wave 2 is schedule to go live in 8/1/2022 one month after Wave I Go-Live. However, a consultant for Budget and Planning (SBP) module has not participated in the O&M and CIP budget sessions in the Explore Phase.	DOH/LSI	Closed	N/A	N/A	LSI may consider a Budget and Planning (SBP) consultant participate in O&M and CIP budget As-is, To-Be and Requirements Analysis sessions in the current Wave I Explore Phase instead of waiting for the scheduled Wave II explore phase. This may minimize duplicated effort for both LSI and DOH, prevent possible rework of solution design and configuration, and assist budget preparation and execution to have seamless integration.	9/2/2021:LSI suggested SBP consultant does not need to participate in the current sessions. Because the go-live dates are only one month apart, it may be suggested that LSI and DOH revisit the schedule to coordinate a simultaneous go-live. 9/30/2021: LSI Project Manager stated that the Go-Live dates of Wave I and Wave II were set based on the DOH budget preparation cycle and the different activities between SBP and FM. 10/15/2021: No major updates. 10/31/2021: SBP resource will join the project soon.	10/31/2021	10/31/2021		
O-210811-01	Observation	M210810-2	8/11/2021	Requirement Management (Processes, Requirements and Fit/Gap)	N/A	New Requirements, Fit / Gap	New requirements are discussed in various explore workshops including Inventory, Plant Maintenance, HR, Grant Management and Payroll modules.	DOH/LSI	Closed	N/A	N/A	Any new requirements discussed during the explore workshops should be documented and included in the Requirement Traceability Matrix. If DOH and LSI decides to implement full blown Inventory, Plant Maintenance, HR, Grants Management and Payroll modules, DOH should establish sets of requirements first before establishing requirements through ad hoc discussions.	9/30/2021: Functions and features of SAP that are not directly related to DOH's RFP requirements are reviewed and discussed in the following business areas: Inventory, Plant Maintenance, HR, Grants Management, and Payroll. Implementation scopes need to be discussed and determined as soon as possible. 10/28/2021: LSI project manager stated during review of logistics master data that no new requirements can be created at this point. Requirements need to be clarified and discrete so that they can be effectively mapped to testing and training for verification and validation. DOH and LSI should ensure the implementation scope and requirements clarification are agreed upon. There may need to be additional discussions. 11/18/2021: LSI consultants will clarify existing and document any new requirements regarding Inventory, Plant Maintenance, HR, Grant Management and Payroll modules in the RTM.	11/18/2021	11/18/2021		
O-210811-02	Observation	M210811-1	8/11/2021	Requirement Management (Processes, Requirements and Fit/Gap)	N/A	Core Requirements for FHWA and DAGS/B&F	The main goal of the DOH FMS project is to implement a new financial management system in compliance with FHWA and the state of Hawaii, DAGS/B&F, and replace the obsolete current mainframe system HWYAC. The Go-Live is set to 7/1/2022, which is a very aggressive plan, and the project team needs to prioritize and focus on must-have requirements.	DOH/LSI	Closed	N/A	N/A	N/A	9/2/2021:The core critical requirements have not been receiving prioritized attention. 9/30/2021: Progress is being made with discussions revolving around core critical requirements, however there are still elements of core critical requirements that need prioritized attention and further discussion about how they will be implemented in SAP. 10/15/2021: No major updates.	10/31/2021	10/31/2021	R-211028-01	
O-210826-01	Observation	M210826-4	8/26/2021	Resource Management	BD	Budget and Planning (SBP) Go-Live and availability of SBP consultant	According to LSI responses to the requirements of Budget Preparation and Budget execution, Budget and Planning (SBP) module was proposed. However, solution design is developed in Fund Management module because SBP will not be available when Wave I goes live on 7/1/2022. The SBP is scheduled to go live on 8/1/2022, one month after the Wave I Go-Live date.	LSI	In Progress	N/A	N/A	It's recommended that LSI provide clear direction and roadmap for how FM will be used instead of SBP during the transition period between Wave I Go-Live and Wave II Go-Live.	10/15/2021: No major updates. 10/31/2021: No major updates. 11/18/2021: No major updates. 12/2/2021: No major updates.	12/2/2021			
O-210826-02	Observation	M210826-5	8/26/2021	Requirement Management (Processes, Requirements and Fit/Gap)	N/A	Solution Design before Completion of Reviewing Requirements.	A high-level solution design is being developed before all of DOH requirements are reviewed.	LSI	Closed	N/A	N/A	It is recommended that LSI complete a thorough analysis of DOH requirements with DOH SMEs, ensure that consultants understand the DOH requirements, and seek out additional clarification and explanation from DOH as needed.	9/30/2021: Progress is made with requirements review and the activities to understand the requirements should be continued. 10/15/2021: General progress is being made. No major updates. 10/31/2021: General progress is being made. No major updates.	10/31/2021	10/31/2021	I-211021-02	
R-210902-01	Risk	M210901-2	9/2/2021	Schedule Management	N/A	Delay in Deliverables	Many LSI deliverables have not been submitted for DOH review/approval on time or they have been delayed. There are more than 20 deliverables scheduled to be completed by the end of the Explore Phase and less than 5 deliverables have been approved by DOH.	LSI	Closed	Low	Low	N/A	9/30/2021: Communication Plan and Organizational Change Management (OCM) Plan deliverables have been submitted and approved. No changes with other documents. 10/15/2021: No major updates.	10/31/2021	10/31/2021	I-211028-01 - I-211028-10	
O-210902-01	Observation	M210902-1	9/2/2021	Schedule Management	N/A	Meeting Schedule	There were few or no meetings occurred on Fridays despite Friday is still a work day for DOH.	DOH/LSI	Closed	N/A	N/A	Fridays could be utilized for meetings and discussions.	9/30/2021: There have been occasional meetings on Fridays. 10/15/2021: No changes. <u>10/31/2021: More meetings occur on Friday.</u>	10/31/2021	10/31/2021		
O-210902-02	Observation	M210902-1	9/2/2021	Schedule Management	N/A	Meeting Schedule	As of 9/2/2021, an access to Sandbox is not available to DOH.	LSI	Closed	N/A	N/A	It is recommended that an access to SAP Sandbox is provided to DOH for DOH users to familiarize themselves with SAP system functions and navigations.	9/17/2021: LSI provided access to SAP Sandbox.	9/30/2021	9/30/2021		

Observation, Risk and Issues (ORI) 12/2/2021																			
ORI ID	Type	LSI Deliverable / ORI Source	Creation Date	Subject Area	Modules	Summary	Description	Responsible Party	Status	Impact	Probability	Feedback / Mitigation		Updates		Review / Target Date	Close Date	Reference ID/Doc	Comments
O-210902-03	Observation	M210826-1	9/2/2021	Resource Management	N/A	Replacement of Billing Consultant	LSI FHWA Billing Consultant is leaving the DOTH FMS project on 9/3/2021.	LSI	Closed	N/A	N/A	It's recommended that LSI replace FHWA Billing Consultant position ASAP and ensure a proper knowledge transfer.		9/9/2021: New AR/FHWA Billing consultant is hired and joining the project.		9/16/2021	9/16/2021		
O-210916-01	Observation	M210915-2	9/16/2021	Requirement Management (Processes, Requirements and Fit/Gap)	N/A	Playback for each module only	Playback sessions are conducted by each module only and DOTH is having a difficult time understanding the full continuous process cycle in SAP.	LSI	Closed	N/A	N/A	DOTH would like to review and validate how SAP processes the entire DOTH business cycle such as PR, PO, Invoice, Payment, to GL posting and reports, etc. in a continuous flow.		9/16/2021: LSI and DOTH agreed that Playback will be conducted based on the DOTH business scenarios. 10/13/2021: LSI consultants demonstrated how SAP processes DOTH requirements from a high level point of view. DOTH submitted its own demo scenarios on 9/30/2021 but they were not part of demonstration that LSI delivered.		10/15/2021	10/15/2021		
O-210923-01	Observation	M210922-1	9/23/2021	Quality Management	N/A	SAP Support Website	DOTH has given access to SAP Support Website. However, no instructions were provided on how to navigate and use the site.	LSI	Closed	N/A	N/A	It is recommended that LSI provide an instruction of how to navigate and utilize the SAP Support Website.		10/15/2021: There is an orientation to SAP Web Support planned for 10/19/2021. 10/19/2021: An orientation to SAP web Support meeting was held.		10/31/2021	10/31/2021		
I-210930-01	Issue	M210929-2	9/30/2021	Schedule Management	N/A	Extension of Explore Phase	LSI extended the Explore Phase one month to complete the explore workshops and deliverables including Document Fit/Gap Analysis, Process Design Documents (PDD) (Documented Business Process Model), and Requirements Traceability Matrix.	DOTH/LSI	In Progress	Medium	N/A	Schedule should be reviewed and adjusted as needed.		10/15/2021: No major updates. 10/31/2021: It is extended again to the middle of November 2021. 11/18/2021: The Explore Phase has not been completed yet. 12/2/2021: The Explore Phase has not been completed yet. There is no specific target date forecasted by LSI.		12/2/2021			
I-211014-01	Issue	M211013-2	10/14/2021	Training and Knowledge Transfer	N/A	Training	LSI provided DOTH key users with access to Sandbox, however, the users were not familiar with how to navigate and enter basic transactions. Project Team Trainings were held in May 2021 but they were more like introductions to SAP with screenshots of SAP data entries and reports. They were not designed to train DOTH Project Team on how to navigate and enter transactions in SAP and they did not include hands-on exercises.	LSI	Closed	Medium	N/A	It is recommended that LSI provide training and instruction on how to navigate and process basic transactions in the Sandbox. This will help DOTH project team to better understand SAP functions and assist with connecting DOTH requirements and business processes to SAP features.		10/19/2021: LSI project manager stated that there won't be any more project team trainings scheduled. DOTH requested one-on-one training with LSI consultants on ad-hoc basis and LSI project manager approved it.		10/31/2021	10/31/2021	O-211028-03	
O-211014-01	Observation	M211014-1	10/14/2021	Requirement Management (Processes, Requirements and Fit/Gap)	INT, PM	Implementation Scope	LSI provided information on available functionalities for Inventory and Plant Maintenance modules for DOTH to decide on the implementation scope.	DOTH	Closed	N/A	N/A	DOTH needs to make a decision on whether or not to implement full scope of Inventory and Plant Maintenance modules.		10/21/2021: DOTH requested that LSI consultants provide more details on how DOTH process will change and what the impact will be for better decision-making. 11/3/2021: DOTH made a decision to include Inventory and Plant Maintenance modules in scope.		11/18/2021	11/18/2021		
O-211014-02	Observation	M211014-1	10/14/2021	Solution Design and Configuration	GM	Implementation Scope	DOTH supplied LSI with full business cycle information on MVSO processes to confirm if GM module fits DOTH needs.	LSI	Closed	N/A	N/A	It is recommended that LSI provide input on the implementation scope of GM module or if an alternative solution is needed.		10/22/2021: LSI consultant informed DOTH that he recommends GM to process MVSO requirements.		10/31/2021	10/31/2021		
I-211014-02	Issue	M211014-1	10/14/2021	Documentation	N/A	Tracking Action Items	Action items in "Open Items Tracker.xlsx" are not monitored or followed up as often as they should be. The last update date of this document was 8/23/2021 as of 10/15/2021.	LSI	Open	High	N/A	Open action items list needs to be updated and monitored regularly in a timely manner and followed through completely and consistently as part of the ongoing project management.		10/31/2021: Action items for both LSI and DOTH should be logged with deadline and they need follow ups. 11/18/2021: No major updates. 12/2/2021: No major updates. It is difficult to get a accurate picture of open items.		12/2/2021			
I-211014-03	Issue	M211014-1	10/14/2021	Resource Management	N/A	Replacement of LSI Financial Lead	LSI financial lead is leaving DOTH H4 project. She has been engaged in this project for more than six months and is the main core consultant who championed DOTH requirements and developed waterfall funding and labor solutions.	LSI	Closed	Medium	N/A	It is recommended that knowledge transfer take place as soon as possible to assist with a smooth transition.		10/25/2021: A new financial lead is onboard on-site and transition is in progress.		11/18/2021	11/18/2021		This issue is no longer applicable.
I-211021-01	Issue	M211021-1	10/21/2021	Interface and Integration	TL	H4 Inbound Interface from HIP	Interface from HIP to SAP for absences transactions and balances is currently not available and will have to be built by ETS upon approval. The request was submitted in Oct 2021 to ETS Governance Committee and ETS will assess the request and announce a result.	LSI	Closed	Medium	N/A	N/A		10/25/2021: ETS informed that it may not be feasible to add absence transactions and balances according to H4 timeline. 10/29/2021: ETS informed that the option of "Existing Interfaces with Modifications" was approved, however the other option of "New Interfaces" was not approved. 11/18/2021: No major updates. 12/1/2021: The H4 Project Team had a meeting with ETS/CherryRoad and resolved the current issue.		12/2/2021	12/2/2021		
I-211021-02	Issue	M211021-3	10/21/2021	Requirement Management (Processes, Requirements and Fit/Gap)	N/A	PDD	It is difficult for DOTH to determine if all of DOTH requirements are properly addressed and included in the correct sections in PDD since they are not cross-referenced in RTM and the requirements are not listed/referenced sequentially in PDD.	LSI	In Dispute	Medium	N/A	It is recommended that when PDD is submitted the corresponding section/module of RTM needs to be completed for DOTH to track requirements coverage, since RTM is referencing PDD.		10/28/2021: LSI project manager stated PDD is to be completed first and RTM is a result of PDD, also PDD is a living document and if there are requirements from RTM that were missed then they will be updated in PDD. 11/18/2021: No major updates. 12/2/2021: No major updates.		12/2/2021			
I-211021-03	Issue	M211021-4	10/21/2021	Requirement Management (Processes, Requirements and Fit/Gap)	N/A	PDD	It is difficult for DOTH users to understand and validate PDD because: - Some requirements were not reviewed and some were not discussed in detail. Clarification and SAP solutions for requirements have not been properly documented. - The project team training was conducted, however it was a generic introduction to SAP using PowerPoint slides. It didn't address DOTH requirements directly. - There were not enough hands-on trainings to understand SAP functions and features. Therefore, DOTH users are having a difficult time applying them to DOTH requirements. - Some DOTH critical core requirements were not discussed early enough in detail and not documented properly.	LSI	Open	Medium	N/A	It is recommended that: - LSI and DOTH should confirm whether all the requirements are reviewed, clarified, and included in PDD. - More training catered to DOTH should be provided. - Core requirements should be considered to be a higher priority.		11/18/2021: No major updates. 12/2/2021: No major updates.		12/2/2021			

Observation, Risk and Issues (ORI) 12/2/2021																	
ORI ID	Type	LSI Deliverable / ORI Source	Creation Date	Subject Area	Modules	Summary	Description	Responsible Party	Status	Impact	Probability	Feedback / Mitigation	Updates	Review / Target Date	Close Date	Reference ID/Doc	Comments
R-211028-01	Risk	M211028-1	10/28/2021	Schedule Management	N/A	PDD	The Go-Live date of 7/01/2022 may not be feasible due to: - Delays in deliverables. - Lack of solution design for DOTH critical core requirements - Lack of focus on DOTH critical core requirements. - Multiple core staff turnover (Project Manager, Fund Management Consultant, Two Assistant Project Managers, FHWA Billing Consultant, Financial/Integration Lead)	LSI	Open	High	N/A	It is recommended that: - Outstanding deliverables should be completed as soon as possible. - DOTH critical core requirements solution design needs to make progress. - DOTH critical core requirements should be higher priority. - Reasons for high turnover should be evaluated.	11/18/2021: No major updates. 12/2/2021: No major updates.	12/2/2021			
I-211028-01	Issue	M211028-1	10/28/2021	Reports and Analytics	N/A	Delay in Deliverables	The Analysis of Reporting Requirements was delayed and has not been completed.	LSI	In Progress	Medium	N/A	It is recommended that LSI complete the deliverable as soon as possible.	11/18/2021: No major updates. 12/2/2021: No major updates.	12/2/2021			
I-211028-02	Issue	M211028-1	10/28/2021	Requirement Management (Processes, Requirements and Fit/Gap)	N/A	Delay in Deliverables	The Requirements Traceability Matrix was delayed and has not been completed.	LSI	In Progress	Medium	N/A	It is recommended that LSI complete the deliverable as soon as possible.	11/18/2021: No major updates. 12/2/2021: No major updates.	12/2/2021			
I-211028-03	Issue	M211028-1	10/28/2021	Training and Knowledge Transfer	N/A	Delay in Deliverables	The End User Training Strategy was delayed and has not been completed.	LSI	In Progress	Low	N/A	It is recommended that LSI complete the deliverable as soon as possible.	11/2/2021: LSI submitted End User Training Strategy and DOTH's review is being in progress. 12/2/2021: DOTH review is being in progress.	12/2/2021			
I-211028-04	Issue	M211028-1	10/28/2021	Requirement Management (Processes, Requirements and Fit/Gap)	N/A	Delay in Deliverables	The Process Design Documents (PDD) (Documented Business Process Model) was delayed and has not been completed.	LSI	In Progress	Low	N/A	It is recommended that LSI complete the deliverable as soon as possible.	11/18/2021: No major updates. 12/2/2021: No major updates.	12/2/2021			
I-211028-05	Issue	M211028-1	10/28/2021	Interface and Integration	N/A	Delay in Deliverables	The Interface Plan was delayed and has not been completed.	LSI	In Progress	Low	N/A	It is recommended that LSI complete the deliverable as soon as possible.	11/18/2021: No major updates. 11/24/2021: LSI submitted and DOTH is reviewing it. 12/2/2021: DOTH requested a revision.	12/2/2021			
I-211028-06	Issue	M211028-1	10/28/2021	Data Conversion	N/A	Delay in Deliverables	The Data Conversion Plan was delayed and has not been completed.	LSI	In Progress	Low	N/A	It is recommended that LSI complete the deliverable as soon as possible.	11/18/2021: No major updates. 12/2/2021: No major updates.	12/2/2021			
I-211028-07	Issue	M211028-1	10/28/2021	Production Migration	N/A	Delay in Deliverables	The Initial Deployment Plan was delayed and has not been completed.	LSI	In Progress	Low	N/A	It is recommended that LSI complete the deliverable as soon as possible.	11/18/2021: No major updates. 12/2/2021: No major updates.	12/2/2021			
I-211028-08	Issue	M211028-1	10/28/2021	Solution Design and Configuration	N/A	Delay in Deliverables	The Technical Infrastructure Plan/Design was delayed and has not been completed.	LSI	In Progress	Low	N/A	It is recommended that LSI complete the deliverable as soon as possible.	11/18/2021: LSI submitted Technical Infrastructure Plan/Design and DED for DOTH's review. DOTH requested a revision due to the document being incomplete and inaccurate. 12/2/2021: No major updates.	12/2/2021			
I-211028-09	Issue	M211028-1	10/28/2021	Requirement Management (Processes, Requirements and Fit/Gap)	N/A	Delay in Deliverables	The Document Fit/Gap Analysis was delayed and has not been completed.	LSI	In Progress	Low	N/A	It is recommended that LSI complete the deliverable as soon as possible.	11/18/2021: No major updates. 12/2/2021: No major updates.	12/2/2021			
I-211028-10	Issue	M211028-1	10/28/2021	Schedule Management	N/A	Delay in Deliverables	The Project Management Plan was delayed and has not been completed.	LSI	In Progress	Medium	N/A	It is recommended that LSI complete the deliverable as soon as possible.	11/18/2021: No major updates. 12/2/2021: No major updates.	12/2/2021			
O-211028-01	Observation	M211028-1	10/28/2021	Solution Design and Configuration	N/A	PDD	Implementation of Inventory and Plant maintenance modules have not been decided. Project Design Document (PDD) does not reflect System/Configuration alternatives on DOTH's decision of whether or not to carry out inventory and plant maintenance module with full implementation scope.	DOTH/LSI	Closed	N/A	N/A	It is recommended that Project Design Document (PDD) include potential system/configuration solutions depending on DOTH's implementation scope decision.	11/3/2021: DOTH made a decision to include Inventory and Plant Maintenance modules in scope.	11/18/2021	11/18/2021		
O-211028-02	Observation	M211028-1	10/28/2021	Risk/Issue Management	N/A	Issue Log	Some items from issue log are being discussed without detailed resolution or follow-up.	DOTH/LSI	Open	N/A	N/A	It is recommended that the issue log be reviewed and discussed in more detail with proper LSI resources and resolution should be discussed the PMO meeting. A separate meeting or inviting the proper LSI resource during the PMO meeting may be required.	11/18/2021: No major updates. 12/2/2021: No major updates.	12/2/2021			
O-211028-03	Observation	M211028-1	10/28/2021	Training and Knowledge Transfer	N/A	Training	DOTH project team members are not familiar with H4 system functions and features for PDD review and having difficulty applying them to DOTH's requirements.	DOTH/LSI	Open	N/A	N/A	It is recommended that DOTH project team members request DOTH-specific one-on-one, hands-on training and question and answer sessions for more familiarity with H4 because the project team training conducted by LSI in May 2021 was based on generic and high-level non-DOTH specific requirements without much detail, nor live system demo with exercises.	11/18/2021: No requests for trainings have been made. Training for the project team members should be conducted as soon as possible. 12/2/2021: No major updates.	12/2/2021			
O-211031-01	Observation	M211028-1	10/31/2021	Resource Management	N/A	Resource Qualification	There are turnovers in LSI project team members. Some team members need more time to understand information related to FHWA and DOT processes.	DOTH/LSI	Open	N/A	N/A	LSI and DOTH should confirm that the consultants meet the qualifications as stated in the RFP, which includes FHWA experience and DOTH equivalent work experience.	11/18/2021: No major updates. 12/2/2021: No major updates.	12/2/2021			
O-211103-01	Observation	M211103-1	11/3/2021	Requirement Management (Processes, Requirements and Fit/Gap)	PM	PM Implementation	Plant Maintenance implementation should not affect Go-Live on 7/1/2021.	DOTH/LSI	Open	N/A	N/A	It is recommended that Plant Maintenance development is scheduled in order to not negatively impact Go-Live date for Wave I. It can go live with Wave II (or it can have its own schedule/Wave). Meanwhile, a manual upload of plant maintenance financial data to GL may need to be considered.	12/2/2021: LSI is reviewing a solution for Plant Maintenance Go-Live date.	12/2/2021			



Observation, Risk and Issues (ORI) 12/2/2021																	
ORI ID	Type	LSI Deliverable / ORI Source	Creation Date	Subject Area	Modules	Summary	Description	Responsible Party	Status	Impact	Probability	Feedback / Mitigation	Updates	Review / Target Date	Close Date	Reference ID/Doc	Comments
I-211108-01	Issue	M211108-1	11/8/2021	Requirement Management (Processes, Requirements and Fit/Gap)	BD	Budget and Planning (SBP)	Budget and Planning (SBP) is a part of the H4 solution and it is supposed to encompass budget transactions, including DOTH's budget prep, execution, A-15, A-19, and A-21. However, LSI proposed that solution design for A-15, A-19, and A-21 will remain in Funds Management until Budget and Planning consultant is available in the future. The H4 Project Team with the SBP consultant will determine the best solution for processing budget maintenance requirements: A-15, A-19, and A-21.	DOTH/LSI	Open	Medium	N/A	It is recommended that H4 Project Team design a permanent solution that will best fit DOTH budget requirements from its first design by engaging the SBP consultant, instead of postponing designing the solution.	12/2/2021: No major updates.	12/2/2021			
O-211115-01	Observation	M211115-1	11/15/2021	Requirement Management (Processes, Requirements and Fit/Gap)	PG	Waterfall Funding Solution	A back-end split waterfall funding solution for FHWA billing is generally more common in the Department of Transportation Highways. However, the Department of Transportation Highways in Hawaii runs on a front-end split waterfall funding with many funds/appropriations. During the procurement process of a new DOTH Financial Management System, LSI proposed and confirmed that a front-end split waterfall funding would fit DOTH's requirements the best. When H4 project started, the financial lead took leadership and discussed a broad overview of how the future front-end split waterfall funding could work in SAP. Soon after, the financial lead left H4 project and LSI confirmed again that a front-end split waterfall funding is still the best solution for DOTH.	LSI	Open	N/A	N/A	N/A	12/2/2021: No major updates.	12/2/2021			
I-211115-01	Issue	M211115-1	11/15/2021 2:D82A82:D82	Resource Management	FB	Consultants for FHWA	Waterfall funding/Split is a core critical requirement for H4, however Waterfall funding/Split was not discussed as much as it should be throughout the Explore Phase. It only started to be discussed recently as an integrated solution during FHWA Billing session.	LSI	Open	Medium	N/A	It is recommended that waterfall funding/Split solution be designed by LSI as soon as possible.	12/2/2021: A whiteboard session is scheduled on 12/8/2021. DOTH is doing another presentation on how DOTH processes Waterfall funding/Split.	12/2/2021			
I-211115-02	Issue	M211115-1	11/15/2021	Resource Management	FB	Consultants for FHWA	Workshops related to Split/Waterfall funding require all consultants to participate because this requirement impacts the various DOTH requirements, including procurement, invoice, payroll, timesheet, project, etc. However, some consultants did not attend the Split/Waterfall-related workshops.	LSI	Open	Low	N/A	FHWA Billing Process starts from cost collection where participation costs are incurred. It involves Fund Management, Requisitions, Purchase Orders, Accounts Payables, and General Ledger. Therefore, respective consultants should attend FHWA related meetings to collaborate and to develop an integrated solution for waterfall funding and FHWA billing.	12/2/2021: No major updates.	12/2/2021			
R-211118-01	Risk	M211118-1	11/18/2021	Solution Design and Configuration	FB	Waterfall Funding Solution	The consultants do not seem to have experience of FHWA with many appropriations and with front-end split. These are unique requirements that Hawaii DOTH have that adds to the difficulty of the project for the consultants to understand the process and design the solution. Some consultants have very limited experience in those fields and it amplifies the difficulty. Some explore sessions showed that there are still areas that require better understanding of the processes.	LSI	Open	Medium	Medium	There may need to be more sessions for a better and full understanding of the FHWA Billing, front-end split, waterfall funding, many-to-many relationship with appropriations and projects, along with any other module or area that need more information for PDD. The H4 Project Team should ensure the implementation consultants meet the qualifications discussed in the RFP.	12/2/2021: No major updates.	12/2/2021			
I-211202-01	Issue	M211202-1	12/2/2021	Quality Management	N/A	Errors, Omission, Inaccuracy in Deliverables	Some LSI Deliverables contained errors and misinformation such as incorrect project name, other client's system architecture, missing/incomplete contents, etc. E.g., Technical Infrastructure Plan/Design, Project Standard Strategy, Scope Management Strategy, etc.	LSI	Open	Medium	N/A	It is recommended that deliverables are more carefully prepared, reviewed and proofread by LSI document quality team before submitting to DOTH for review.					
I-211202-02	Issue	M211202-1	12/2/2021	Quality Management	N/A	Process Flow Formatting	Consultants worked on PDDs based on their responsible business areas. However, Process Flows Diagrams are not standardized in PDDs.	LSI	Open	Low	N/A	N/A					
